BY ORDER OF THE COMMANDER
EDWARDS AIR FORCE BASE

EDWARDS AIR FORCE BASE
INSTRUCTION 99-101

21 APRIL 2026

Test and Evaluation

TEST PLANS

COMPLIANCE WITH THIS PUBLICATION IS MANDATORY

ACCESSIBILITY: Publications and forms are available on the e-Publishing website at www.e-Publishing.af.mil for downloading or ordering

RELEASABILITY: There are no releasability restrictions on this publication

---

OPR: 412TW/TENG

Certified by: 412TW/CT
(Daniel Osburn)

Supersedes: EDWARDSAFBI99-101, 15 September 2016

Pages: 16

This Edwards Air Force Base Instruction (EDWARDSAFBI) implements Department of the Air Force Instruction (DAFI) 99-103, *Capabilities-Based Test and Evaluation*, by establishing responsibilities and local procedures for the development, review, and approval of test plans for the 412th Test Wing (412 TW). The goal is to develop technically robust test plans that provide relevant, high-confidence planning. It applies to all test plans where 412TW resources will be used or are at-risk, even when the 412TW has no technical analysis and reporting responsibility. This instruction does not require tiers at or below the Wing level. Waiver authority for this instruction is 412 TW/CT. This instruction addresses development, review, and approval of test plans from a technical point of view. Test safety planning and review is covered by the Air Force Test Center Instruction (AFTCI) 91-202, *Air Force Test Center Test Safety Review Process* and

AFTCI 91-202_412TWSUP, *412th Test Wing Test Safety Review Process*. Technical reporting is covered by EDWARDSAFBI 99-103, *412TW Technical Report Program*. This Instruction requires the collection and or maintenance of information protected by the Privacy Act of 1974 authorized by Title 10, United States Code, Section 8013, and the Personnel Data System (PDS). The applicable Air Force Privacy System of Records Notices (SORN) F033 AF A, Information Request-Freedom of Information Act. Ensure all records created as a result of processes prescribed in this publication are maintained in accordance with AFI 33 322, Records Management and Information Governance Program, and disposed of in accordance with the Air Force Records Information Management System (AFRIMS) Records Disposition Schedule located at **https://afrims.cce.af.mil/**. Maintain all records created as a result of processes described in this publication in accordance with (IAW) AFI 33-322, *Records Management and Information*

Governance Program, and disposed of IAW Air Force Records Information Management System Records Disposition Schedule. Any name or mark of a manufacturer, commercial product, commodity, or service in this publication does not imply endorsement by the Air Force.

SUMMARY OF CHANGES

This document has been substantially revised and must be completely reviewed. The primary changes include the clarification of various forms of technical review documentation and processes.

1. Policy. 3
2. Responsibilities. 3
3. Procedures. 5
4. Test Plan Changes. 10
5. Closure. 12

Attachment 1—GLOSSARY OF REFERENCES AND SUPPORTING INFORMATION 13

Attachment 2—412TW TEST PLAN PROCESS OVERVIEW 15

Attachment 3—TECHNICAL RISK LEVELS 16

1. Policy.

1.1. Test plans are required for all tests in which 412TW resources (personnel, aircraft, equipment, facilities, etc.) will be utilized or are at risk.

1.1.1. A test can be a ground or flight activity to gather specific information, answer a customer's question, or provide information not wholly covered by an approved instruction manual. Test is defined as the act of generating empirical data during the research, development, or sustainment of systems, and the creation of information through analysis that is useful to technical personnel and decision makers for reducing design and acquisition risks.

1.2. All test plans involving 412TW resources will receive an independent technical review or Reasonable Use of Government Resources (RUGR) statement. Test plan categories include:

1.2.1. 412TW authored test plans.

1.2.1.1. The 412TW authored test plans for tests conducted by the 412TW and for which the 412TW has technical analysis and reporting responsibilities must include the content outlined in this instruction.

1.2.2. Non-412TW authored test plans.

1.2.2.1. Non-412TW-authored test plans in which the 412TW has technical analysis and reporting responsibility should either include content outlined in this instruction or a Chief Engineer authored Memorandum for Record (MFR) that provides insight into the missing content.

1.2.3. Tests in which the 412TW has no technical analysis or reporting responsibility.

1.2.3.1. When the 412TW is a participating test organization or does not have technical analysis and reporting responsibilities, test plans must contain sufficient content and detail for the technical review authority (TRA) to determine whether: 1) the tests are a reasonable use of 412TW resources, and 2) there are any significant technical risks.

1.3. Changes to existing test plans must be reviewed IAW Section 4 of this instruction.

1.4. Prior to testing, an independent safety review of all test plans is required to identify potential hazards, determine risk mitigations, and assess residual risk IAW AFTCI 91-202 for all tests utilizing 412TW assets. This is usually accomplished by the Safety Review Board (SRB). The documentation containing the test and safety plans is referred to here and in AFTCI 91-202 as the test package. Reference AFTCI 91 202 and AFTCI 91 202_412TWSUP for safety planning, review, and approval requirements. Both technical and safety reviews (up to and including approval) must be completed before testing begins.

2. Responsibilities.

2.1. 412TW Leadership.

2.1.1. Review, concur, and/or approve test packages IAW AFTCI 91-202.

2.1.2. Assign a 412TW test unit as a liaison to assist non-412TW organizations seeking approval to test using 412TW resources.

2.2. 412TW Technical Director (412 TW/CT).

2.2.1. Set policy for the test plan development, review, and approval process.

2.2.2. Ensure all test plans utilizing 412TW resources receive an independent technical review. The 412 TW/CT may keep technical review authority or may designate a 412TW engineering group, engineering squadron, or equivalent as the TRA. TW/CT assigns TRA for USAF Test Pilot School (TPS) student Test Management Project (TMP) test plans to TPS/CT unless TPS/CT determines a higher level of TRA is required.

2.2.2.1. If the TRA does not have expertise in all the test areas to ensure adequate review of the test plan, the TRA shall request assistance from the appropriate 412TW organizations.

2.2.2.2. The TRA will ensure an independent technical review is accomplished IAW Department of Defense instruction (DoDI) 5000.89_DAFI99-103_AFMCSUP and this instruction.

2.2.3. Assess whether the test is a RUGR.

2.3. Independent Technical Reviewers (ITRs) (technical experts from 412TW engineering, operations, and maintenance/logistics organizations). The ITRs review test plans to meet technical standards and provide experiential guidance.

2.3.1. Support the 412TW test plan technical review process IAW this instruction.

2.3.2. The ITRs should be from outside the test unit whenever possible but may be from within the test unit if independent from the test project (i.e., not a project engineer or project aircrew/operator for the test). In both cases, the ITRs must neither have a vested interest in the successful accomplishment of the test objectives nor be directly responsible for the development and preparation of the test plan or safety plan, nor be the Test Execution Authority.

2.3.3. Should be senior in test experience with applicable knowledge and sufficient expertise in the test activity to be reviewed.

2.3.3.1. Operations Reviewers should be experienced in the type of system under test such as aircraft (e.g., fighter, bomber, or cargo), ground test facility (e.g., wind tunnel, sled track, propulsion stand, or climatic lab), and the types of tests being conducted. These reviewers ensure tests are executable, all test techniques are considered, and the most effective/efficient techniques are selected.

2.3.4. To the maximum extent possible, ITRs should be the same individuals who are projected to serve as independent safety reviewers for the safety review.

2.4. Combined Test Force Commander/Director (or equivalent).

2.4.1. For the purposes of this instruction, a Combined Test Force (CTF) is any test force or unit conducting test.

2.4.2. Support the 412TW test plan technical review process. Ensure CTF discipline engineers and air crew/operator (e.g., project pilot) support technical reviews of the projects to which they are assigned. When requested, CTF aircrew and other personnel are required to provide independent reviews of other test programs or activities.

2.5. CTF Chief Engineer (or equivalent).

2.5.1. Train, guide, and direct test teams to ensure proper test plan development.

2.5.2. Request expert technical assistance from appropriate 412TW engineering offices as early as possible during test plan development to ensure the best possible test plan.

2.5.3. Ensure 412TW engineering personnel comply with this instruction in preparing test plans and making thorough and timely test plan inputs.

2.5.4. Ensure test plans are prepared IAW this instruction and are of sufficient quality before they are submitted for technical review. Ensure test plans are submitted for technical reviews in time to allow comprehensive technical and safety reviews and to meet program requirements and schedules.

2.5.5. Ensure completion of technical review action items and incorporation of recommended test plan changes. Whenever exceptions exist, as described in Section 3.4.1.3., document the rationale for the exceptions and incorporate this document into the test package as described in Section 3.4.2.

2.5.6. Ensure proper test plan distribution after approval.

2.5.7. Identify the Project Engineer/Project Test Lead.

2.6. Project Engineer/Project Test Lead.

2.6.1. Ensures requirements of this instruction are met during all phases of test.

2.6.2. Serves as the test team point of contact.

2.7. Project Test Team.

2.7.1. Drafts the test planning documentation (e.g., test plan and safety plan).

2.7.2. Supports the Project Engineers and Chief Engineers as directed.

2.8. Technical Expert Organizations (412 TENG, 412 EWG, 412 MXLS, USAF TPS, etc.).

2.8.1. Provide expertise to aid in test planning, develop analysis capabilities, support technical reviews, and train testers in all aspects of the process described in this instruction.

3. Procedures.

3.1. Overall Process. The intent of a technical review is to conduct an independent technical assessment and executive-level review of the test plan, which involves three general categories: planning, review, and submission for approval. The 412 TW's final approval of the test plan occurs when the test package is approved IAW AFTCI 91-202. When the Chief Engineer (or equivalent) deems the plan ready for independent review, he/she submits it with a request for review to 412 TW/CT. The independent technical review is conducted by 412 TW/CT or his/her delegate. After the review is completed, recommendations and action items are provided to the test team. The test team provides the updated version of the plan along with their responses to recommendations and action items to the TRA. The TRA generates a technical review memorandum (TRM) to document the technical adequacy of the test plan and any residual technical risk. **Attachment 2** shows the overall process for test plan development. **Attachment 3** provides technical risk level definitions.

3.2. Developing the Test Plan. The CTF Chief Engineer will ensure that a test plan is developed to meet the test objectives mutually agreed upon by the 412 TW, the customer, and/or other participating agencies.

3.2.1. Test plans may be created in a variety of formats. Regardless of format, 412TW authored test plans must, and non-412TW authored test plans should contain: test objectives, test techniques, scientific test and analysis techniques or statistical methods, test configurations and conditions, limitations, instrumentation requirements, and management information. Test plans document why tests will be accomplished (the test objectives), how tests will be accomplished (the test techniques and test points), what data will be acquired (the instrumentation requirements), why the test may not be completed as designed (limitations as applicable), when and what type of report is needed (management information) and how data will be used to answer the test objectives (data analysis plan). Non-412TW authored test plans that do not include this information should be accompanied by rationale from the CTF Chief Engineer that provides insight into the missing items.

3.2.2. Use of statistical methods. Test teams will include in the test plan, or equivalent document, a statement regarding whether statistical methods are used. When statistical methods are used, the statement will highlight the applicability to the test as well as any limitations of the methods to be used. When statistical methods are not used, the statement will include the reason.

3.2.2.1. Test teams shall work with statisticians from the 812 Test Support Squadron (TSS) and technical experts to incorporate statistical methods when planning tests. If statistical analysis is not planned, justification must be provided in the test plan or an equivalent document.

3.2.3. Data Analysis Plan (DAP). The DAP should be developed as a part of the planned test effort but does not necessarily need to be a part of the test plan. Regardless of format, the DAP should convey clear progression from raw collected data to the final data product in the technical report. The DAP should capture the validated algorithms for data reduction, analysis, and final data products prior to testing. Each engineering discipline should have detailed requirements for appropriate DAP content. When appropriate, the DAP includes statistical power and confidence (or other statistical measures of merit) for measures of performance, the test conditions believed to influence system performance (including which conditions will be measured and recorded, which conditions will be varied, and which conditions will be held constant), and the number of test points (including justification of selected test points).

3.3. Review of the Test Plan. To ensure proper and adequate preparation and planning, a thorough technical review of test planning documentation is required. For test plans in which the 412TW has analysis and/or reporting responsibility, the technical review process will assess reporting requirements, the report schedule, and the DAP in addition to other test plan elements.

3.3.1. When a test plan is ready for independent review, the Chief Engineer will send a request for technical review to the 412 TW/CT. The request for technical review will include a test plan summary, reporting requirements, and analysis/reporting schedule.

3.3.2. The 412 TW/CT will retain the TRA at the Wing level or designate an engineering group or squadron as the TRA via written request.

3.3.3. Technical Review. The TRA shall conduct a technical review. In accordance with DODI5000.89_DAFI 99-103_AFMCSUP, "At a minimum, technical reviews will assess test requirements, techniques, approaches, and objectives." The technical review will also ensure that environmental analyses have been completed, as required by DAF Policy for Implementation of the National Environmental Policy Act (NEPA), and are referenced in the test plan.

3.3.3.1. Technical review boards (TRBs) are the expected means for technical review. This is especially true when: there are multiple engineering disciplines involved; the test, analysis, or system under test are especially complex; envelope expansion or other elevated risk testing is involved; and/or new test or analysis methods will be applied. The TRA will serve as the TRB Chairperson. Review methods other than a TRB must be approved by 412 TW/CT.

3.3.3.1.1. The test team may request a combined TRB/SRB in lieu of separate technical and safety reviews to minimize impact to resources and shorten review timelines. The TRA and the Test Safety Office together provide the final determination on this course of action. Teams will ensure that the test plan is sufficiently mature for safety review prior to the combined TRB/SRB, per AFTCI 91-202. In cases where a combined TRB/SRB is elected, teams will work with both the TRA and the SRB Chairperson to schedule the meeting.

3.3.3.1.2. The TRA will ensure that the board consists of experienced personnel to include at least one or more independent representative(s). Additionally, the board shall include an experienced, independent operations representative unless deemed unnecessary, as approved by the TRA. The TRA will also ensure the TRB board includes a member of the 812 TSS Statistical Methods Flight when appropriate.

3.3.3.1.3. The technical review board comprises experienced personnel not directly associated with the execution of the project to provide test plan development. The TRB members will be chosen based on their experience in the areas addressed in the test plan. The member's expertise should not be limited to the test program objectives but should be broad enough to critically review all aspects of the planned test.

3.3.3.1.4. The Chief Engineer, operations, and engineering test team personnel will support and participate in the review as consultants. Appropriate customer and contractor representatives may also be invited. The Project Engineer/Project Test Lead shall coordinate with the TRA to determine the date for the TRB and will arrange availability of a suitable meeting location. Test teams will provide test plan

read-ahead copies 5 working days (preferred) to 3 working days (minimum) prior to the TRB, unless otherwise approved by the TRA. In all cases, all reviewers must have had adequate time to review the documents before the start of the technical review. The test team will coordinate a realistic and attainable review timeline with the TRA and board members. The TRA, in consultation with the TRB board members, will determine if there is sufficient time for review.

3.3.3.1.5. The default venue for a TRB is a conference room with all board members and test team and consultant representatives present in person, but TRBs may be accomplished virtually with approval from 412 TW/CT.

3.3.3.2. An alternative to a TRB is a serial technical review that occurs without a meeting. The test plan is typically distributed electronically and reviewed in parallel by the TRB members. A serial technical review may be appropriate for test activities that are readily understood by reviewers, are lower in complexity, and are expected to be deemed lower in risk. If a serial technical review is approved by 412 TW/CT, the TRA shall ensure that a thorough independent review is accomplished, and any feedback is provided to the responsible test team. When a TRB meeting is not convened, the test team will support the serial technical review process by maintaining communication with the TRA and providing responses to reviewer questions and requests as soon as possible.

3.3.4. Reasonable Use of Government Resources. The Chief Engineer for the test project shall review the test plan to establish that the 412TW has no technical responsibility (no analysis is to be conducted or a report with assessment and/or ratings is not to be produced). The Chief Engineer will ensure that the pertinent technical reviewer(s) has/have reviewed the test plan, identified any significant technical risks, concur with the content, and that the 412TW has no technical responsibility.

3.3.4.1. The Chief Engineer shall summarize the key points of the testing to be performed and the rationale behind why they believe the test effort is a RUGR in communication to 412TW/CT (who retains TRA) and request determination of RUGR. This may include multiple non-412TW authored test plans serving a single test effort.

3.3.4.2. A TRB may be held at the discretion of the Chief Engineer when a heightened level of technical review is warranted.

3.3.4.3. If 412 TW/CT decides the test activity is a reasonable use of government resources with no report or evaluative responsibilities, they shall respond in an email or MFR to the Chief Engineer with their concurrence of the designation via a RUGR statement.

3.3.4.4. If 412 TW/CT does not concur with the RUGR designation, then 412 TW/CT will follow the process laid out in Section 3.3.3.

3.4. Finishing and Submitting Test Plan for Approval.

3.4.1. Technical Review Memorandum (TRM). Following the technical review, the TRA will generate a TRM summarizing the technical review. When the 412TW is the executing test organization, the TRM shall state whether a test plan is considered technically adequate to meet the stated test objectives, whether there are significant technical risks, and shall

include a statement regarding the level to which statistical test techniques or methods have been applied. If so delegated, the TRA will provide a copy of the TRM to 412 TW/CT. When the 412TW does not have technical analysis and reporting responsibilities, the RUGR statement from 412 TW/CT will indicate whether a test plan is a reasonable use of 412TW resources and serve as the TRM.

3.4.1.1. The TRA will use the TRM to document: who conducted the review, the current technical status and risks of the test plan, any additional recommendations and/or open action items, whether the test team considered the statistical relevance of their approach in the test design, and the test reporting plans. In the TRM, the TRA should determine test plan status as follows: adequate to meet the test objectives; adequate to meet the test objectives after recommended changes are incorporated; or 412TW analysis or reporting inadequate to meet the test objectives. If 412TW analysis and/or reporting are determined to be inadequate to meet the test objectives, the TRA must notify the 412 TW/CT as soon as possible.

3.4.1.1.1. Technical Adequacy. Technical adequacy is the determination that the planned test methods, data and analysis techniques, resources, and execution approach meet the stated objectives and support program requirements.

3.4.1.1.2. Technical Risk. Technical risk is the assessment of credible factors that could adversely impact meeting the test plan's objectives. It involves uncertainties or limitations regarding the technical approach, technologies, or capabilities that could affect the ability to meet the stated objectives. **Attachment 3** provides technical risk level definitions that are used only if the test plan is deemed technically adequate.

3.4.1.2. When a TRB is held, the TRM attachments will, at a minimum, include the TRB summary document with action items and attendance list. The action items will be provided along with the test team responses and closure status as judged by the TRA.

3.4.1.3. The test team will modify the test plan to incorporate the appropriate recommendations from the technical review. If there are recommendations or action items that are not addressed in a test plan change, the exceptions will be noted in the TRM. The test team will provide reasons for the exceptions to the TRA so that they can be incorporated in the TRM. In the case of exceptions to recommendations or action items, the TRA will notify the 412 TW/CT when providing the copy of the TRM so that increased technical risk can be noted and addressed.

3.4.2. Test Package Preparation. Following the issuance of the TRM, the CTF Chief Engineer will ensure that the test team provides the test plan with its signature page ready for signing prior to the SRB that includes, at a minimum, the primary author and the Chief Engineer signatures. The package will also include the completed and signed TRM. If any exceptions exist, an MFR explaining reasons for exceptions to TRB recommendations or action items will be generated. These documents will be included in the test package IAW AFTCI 91 202.

3.4.3. Test Plan Changes Prior to Test Package Approval. Test plan changes will not be documented through the amendment process until the test package has been approved IAW AFTCI 91 202. Therefore, test plan changes that occur following TRM issuance but prior to test package approval are permitted without amendment and require review by the TRB chairperson to determine if they fall within the scope of the TRM. If the TRB chairperson determines the changes are within the scope of the current TRM, then no further action will be required. If the TRB chairperson determines the changes are out of scope of the current TRM, a follow-on TRB may be required, along with issuance of a new TRM.

3.5. Test Plan Approval. The test plan will be approved as part of the test package IAW AFTCI 91-202.

3.6. Test Plan Distribution. After test package approval, the Chief Engineer shall ensure distribution of the approved test plan to: Defense Technical Information Center (DTIC), the Edwards AFB Technical Research Library, the 412TW History Office (412 TW/HO), the TRA, and to organizations requiring the test plan for participation or support. Test Pilot School student TMP test plans are part of the instructional process and thus will not be distributed to DTIC, 412TW/HO, or the Edwards AFB Technical Research Library. These plans will be archived, if required, within TPS and are considered TPS internal-use documents.

4. Test Plan Changes.

4.1. The CTF Chief Engineer shall ensure that the test team documents test plan changes and rationale thereto. For both minor and major changes, the office responsible for the original technical review (the original TRA) shall be provided with a copy of the modified test plan and the change documentation. The CTF Chief Engineer shall ensure the unit consults with the TRA to determine whether a change is minor or major and if the changes affect the technical adequacy of the test plan. For administrative changes, concurrence must be provided from the CTF Chief Engineer or TRA. Test package changes, whether to the test plan or safety plan, are documented and approved IAW AFTCI 91-202. Modifications to the data analysis plan alone are not considered test plan changes but should be communicated with the TRA and pertinent ITR(s).

4.1.1. Changes for Test Packages Operating under a RUGR. Determination of whether a change is minor or major falls to the CTF Chief Engineer. If the change is considered major, the change shall be sent to 412 TW/CT for determination of whether a new RUGR is required.

4.2. Major Changes. A major change is defined as any substantive change to test objectives, technical approach or test methodology, or changes to test procedures or test scope, such that the original TRM is no longer valid. For a major change, the technical review and approval processes are identical to that for the original test plan. Based on the change documentation provided by the Chief Engineer, the TRA will determine whether a TRB meeting is required. In determining the need for a TRB meeting, the TRA will consider the extent of the changes, results of testing to date, predicted results of proposed testing, and other pertinent details. The TRA will document the results of the technical review in a TRM, as outlined in **paragraph 3.4.1**. The TRM and any associated additional documentation must be included in the test package when it is amended IAW AFTCI 91-202.

4.2.1. Major Changes For test packages operating under a RUGR. In addition to definitions in 4.2, a major change is defined as substantively changing the extent or type of government resources in use.

4.3. Minor Changes. Minor changes are those that are within the technical scope of the previously approved package. Examples may include changing flight conditions of test points as long as they remain close to existing test points and within the envelope of test points approved in the most current test plan, adding test points within the envelope of test points and technical scope approved in the original plan, and deleting test points if preliminary results validated by a technical expert show they are unnecessary and are not part of a safety build-up. Other than the previously mentioned review to determine change category, a minor change does not require a new technical review. The change shall be documented and the coordination/approval process for the amendment will be IAW AFTCI 91-202. The test team shall provide a copy of the amendment to the TRA and add the amendment to the test package when it is approved. Minor changes do not require an update to the TRM.

4.3.1. Pre-Approved Minor Changes. A new approval is not required for a minor test plan change if 1) the TRA has permitted minor changes to the test plan as documented in the TRM and 2) the Chief Engineer (or equivalent) or the platform technical expert concur that the test plan change is minor. Coordination with other reviewers may also be required at the discretion of the CTF Chief Engineer or the platform technical expert. The TRA has the authority to pre-approve all minor changes or limit the scope of pre-approved minor changes. The TRA shall state the scope of what is permitted as a pre-approved minor change via the TRM. Pre-approved minor changes made to the test plan are documented IAW AFTCI 91-202.

4.3.2. For test packages operating under a RUGR, a minor change is defined as not affecting the extent or type of government resources in use.

4.4. Administrative Changes. An administrative change clarifies information contained in the test plan and does not affect the technical approach to testing. Administrative changes to the test plan shall be documented IAW AFTCI 91-202.

4.4.1. Any change to the test plan may be an indication of inadequate technical planning, no matter how small the change originally appears. The test team and TRA must thoroughly question the background and implications of all administrative changes to ensure they would not benefit from additional review.

4.4.2. The test plan author may make administrative changes directly to the test plan.

4.4.3. The TRA and 412 TW/SET will be notified of all administrative changes to the test plan.

4.4.4. I99-100For test packages operating under a RUGR, an administrative change is defined as in 4.4 and does not require change documentation.

4.5. Change Approval and Distribution. Test package amendments will be approved IAW AFTCI 91-202. The CTF Chief Engineer shall ensure distribution of the approved test plan to organizations requiring the plan for participation or support within the restrictions of the distribution statement and classification.

5. Closure.

5.1. As indicated in AFTCI 91-202, the closure amendment is the final step in the overall test and safety review process. At the time the closure amendment is generated, the final version of the test plan will be archived in DTIC and the Edwards AFB Technical Research Library.

THOMAS M. TAUER, Colonel, USAF
Commander, 412th Test Wing

Attachment 1

GLOSSARY OF REFERENCES AND SUPPORTING INFORMATION

References

DODI5000.89_DAFI99-103_AFMCSUP, *Capabilities-Based Test and Evaluation*, 17 October 2022

AFTCI91-202, *Air Force Test Center Test Safety Review Policy*, 23 November 2022

AFTCI91-202_412TWSUP, *412th Test Wing Test Safety Review Policy,* 16 February 2023

EDWARDSAFBI99-103, *412TW Technical Report Program*, 9 March 2026

AFI33-322, *Records Management and Information Governance Program*, 28 Jul 2021

SAF/IEI Memorandum, *Initial Department of the Air Force (DAF) Policy for Implementation of the National Environmental Policy Act (NEPA*), 7 July 2025

Adopted Forms

AF Form 847, *Recommendation for Change of Publication*

AFTO Form 22, *Technical Manual Change Recommendation and Reply*

AFTO Form 27, *Preliminary Technical Order (PTO) Publication Change Request (PCR)/TO Verification Record/Approval*

SF 298, *Report Documentation Page*

Abbreviations and Acronyms

AF—Air Force

AFB—Air Force Base

AFMCSUP—Air Force Materiel Command Supplement

AFTCI—Air Force Test Center Instruction

CTF—Combined Test Force

DAFI—Department of the Air Force Instruction

DAP—Data Analysis Plan

DoD—Department of Defense

DoDI—Department of Defense Instruction

DTIC—Defense Technical Information Center

EDWARDSAFBI—Edwards Air Force Base Instruction

IAW—In Accordance With

ITR—Independent Technical Reviewer

MFR—Memorandum for Record

OPR—Office of Primary Responsibility

RUGR—Reasonable Use of Government Resources

SRB—Safety Review Board

TMP—Test Management Project

TPS—Test Pilot School

TRA—Technical Review Authority

TRB—Technical Review Board

TRM—Technical Review Memorandum

TSS—Test Support Squadron

TW—Test Wing

USAF—United States Air Force

412 TENG—412th Test Engineering Group

412TW—412th Test Wing

412 TW/CC—412th Test Wing Commander

412 TW/CT—412th TW Technical Director


412 TW/HO—History Office

Attachment 2

412TW TEST PLAN PROCESS OVERVIEW

A2.1. The 412TW test plan process is specified in Figure A2.1.

Figure A2.1. 412TW Test Plan Process Overview.

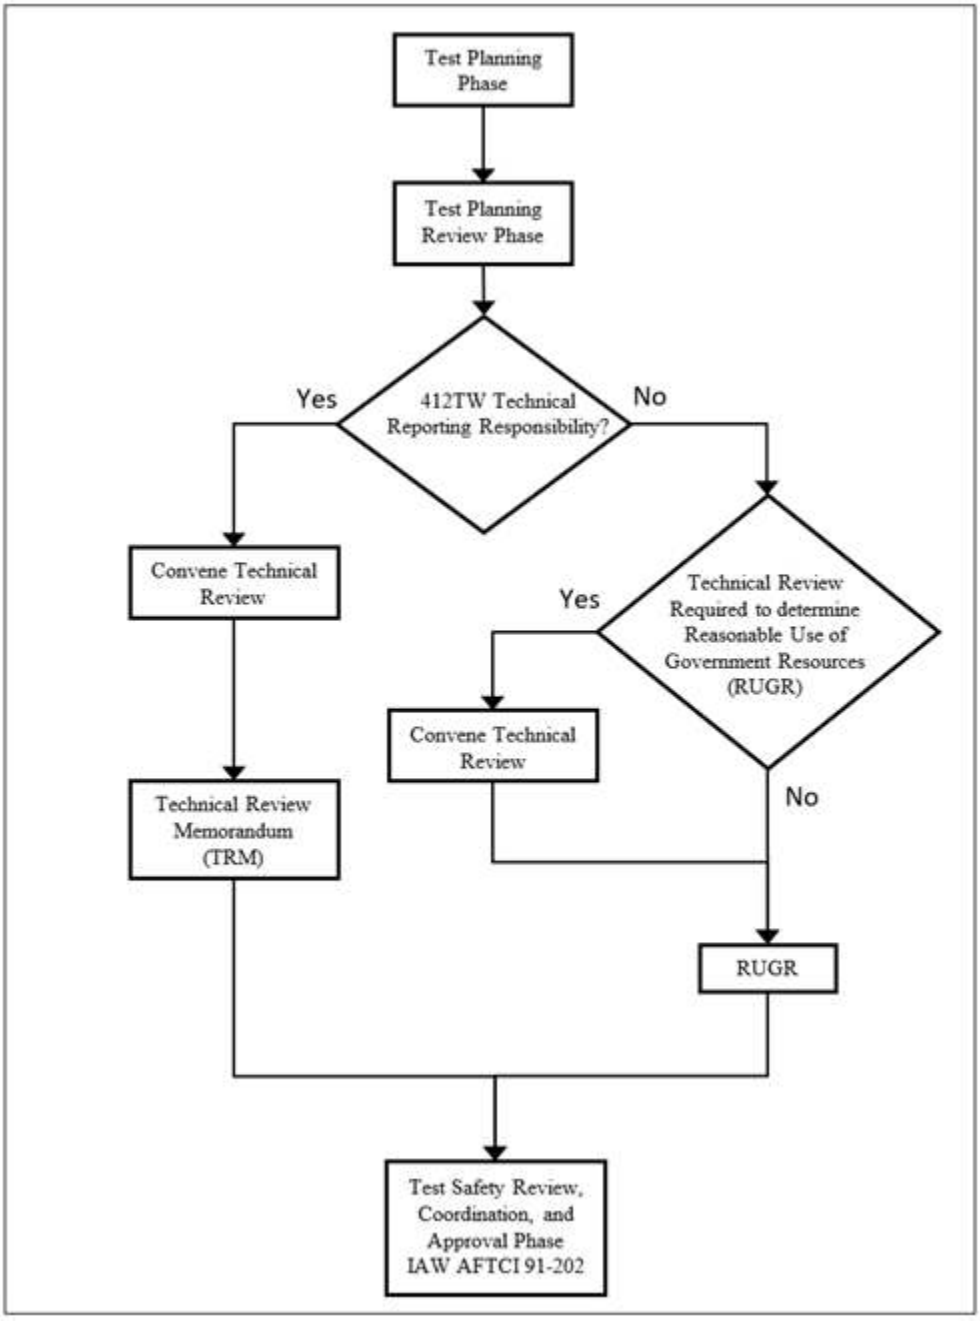

Attachment 3

TECHNICAL RISK LEVELS

Table A3.1. Technical Risk Levels.

Technical Risk Level	Description and Implication
HIGH	Factors present significant potential to adversely impact the ability to meet the test objectives. Significant uncertainties and limitations are known and are largely uncontrolled. Achieving the stated objectives may not be likely.
MEDIUM	Factors present moderate potential to adversely impact the ability to meet the test objectives. Some uncertainties or limitations are known and/or partially controlled. The likelihood of meeting the objectives is questionable.
LOW	Factors present little or no potential to adversely impact the ability to meet the test objectives. Most uncertainties or limitations are known and controlled. There is confidence in achieving the objectives as planned.
