BY ORDER OF THE SECRETARY OF THE AIR FORCE

SPACE FORCE MANUAL 63-142

1 OCTOBER 2026

Acquisition

WEAPON SYSTEM SUSTAINMENT PORTFOLIO PROCEDURES

COMPLIANCE WITH THIS PUBLICATION IS MANDATORY

ACCESSIBILITY: This publication is available for downloading or ordering on the e-Publishing website at www.e-Publishing.af.mil

RELEASABILITY: There are no releasability restrictions on this publication

---

OPR: CFC/S4

Certified by: SAF/AQ
(William D. Bailey)
Pages: 49

This Space Force Manual (SPFMAN) implements and identifies Weapon System Sustainment (WSS) portfolio procedures referenced in Department of the Air Force Instruction (DAFI) 63-101/20-101, *Integrated Life Cycle Management*. It provides guidance and procedures on WSS requirements to inform resourcing decisions. This publication applies to all civilian employees and uniformed members of the United States Space Force and those with a contractual obligation to abide by the terms of Department of the Air Force (DAF) issuances, except where otherwise noted. This publication does not apply to the United States Air Force, Air Force Reserve, or Air National Guard. Ensure all records generated as a result of processes prescribed in this publication adhere to Air Force Instruction 33-322, *Records Management and Information Governance Program*, and are disposed in accordance with the Air Force Records Disposition Schedule, which is located in the Air Force Records Information Management System. Refer recommended changes and questions about this publication to the office of primary responsibility using the DAF Form 847, Recommendation for Change of Publication; route DAF Forms 847 from the field through the appropriate functional chain of command. This publication may be supplemented at any level, but all supplements must be routed to the office of primary responsibility of this publication for coordination prior to certification and approval. Compliance with attachments **2**, **3**, **4**, **5**, **and 6** in this publication is mandatory. The authorities to waive wing, unit, or delta level requirements in this publication are identified with a tier ("T-0, T-1, T-2, T-3") number following the compliance statement. Submit requests for waivers through the chain of command to the appropriate tier waiver approval authority, or alternately, to the publication OPR for non-tiered compliance items. The use of the name or mark of any specific manufacturer, commercial product, commodity, or service in this publication does not imply endorsement by the DAF.

Chapter 1—INTRODUCTION **4**

1.1. Overview. 4

1.2. Applicability. 4

1.3. Scope. 4

1.4. WSS Governance. 4

1.5. WSS Process. 5

Figure 1.1. The WSS Process. 6

1.6. Program Entry to WSS. 7

Chapter 2—ROLES AND RESPONSIBILITIES **8**

2.1. Assistant Secretary of the Air Force for Space Acquisition and Integration (SAF/SQ). 8

2.2. Deputy Chief of Space Operations for Operations (SF/S3/4/7). 8

2.3. Deputy Chief of Space Operations for Strategy, Plans, Programs, and Requirements (SF/S5/8). 9

2.4. Deputy Chief of Space Operations for Intelligence (SF/S2). 9

2.5. Field Commands (FLDCOMs): SSC, CFC, and STARCOM. 9

2.6. Portfolio Acquisition Executives. 10

2.7. Program Offices. 10

2.8. WSS Executive Agent. 11

Chapter 3—LOGISTICS REQUIREMENTS DETERMINATION PROCESS (LRDP) **14**

3.1. Overview. 14

Figure 3.1. LRDP Process. 14

3.2. Phase One – Prepare Requirements. 14

3.3. Phase Two – Define Requirements. 14

3.4. Phase Three – Requirements Collaboration. 14

3.5. Phase Four – Prioritize Requirements. 14

3.6. Phase Five – Publish Requirements. 14

3.7. General Requirements Management. 15

Chapter 4—PROGRAM OBJECTIVE MEMORANDUM (POM) PROCESS **18**

4.1. Overview. 18

Figure 4.1. POM Phases. 18

4.2. Phase One – Preparation. 19
4.3. Phase Two – Development. 19
4.4. Phase Three – Review, Validation, and Adjustment. 20
4.5. Phase Four – Approval. 20
Chapter 5—EXECUTION PLAN (EXPLAN) PROCESS **22**
5.1. Overview. 22
Figure 5.1. ExPlan Process. 22
5.2. Phase One – Preparation. 22
5.3. Phase Two – Development. 23
5.4. Phase Three – Review, Validation, and Adjustment. 23
5.5. Phase Four – Approval. 24
5.6. Post-approval Activities. 24
Chapter 6—EXECUTION PROCESS **25**
6.1. Overview. 25
Figure 6.1. Execution Activities Timeline. 25
6.2. Weapon System Sustainment Requirements. 25
6.3. Funding. 25
6.4. Forecast and Actual Obligation Updates. 27
6.5. Requirement Changes. 27
6.6. Unfunded Requirement Requests. 28
Attachment 1—GLOSSARY OF REFERENCES AND SUPPORTING INFORMATION **30**
Attachment 2—PROGRAM ENTRY TO WSS DECISION TREE **38**
Attachment 3—RISK CATEGORY DESCRIPTIONS **40**
Attachment 4—PROGRAMMATIC FAILURE POINT DEFINITIONS **44**
Attachment 5—REQUIREMENT CHANGE THRESHOLD AND APPROVAL CRITERIA **45**
Attachment 6—EMERGING SPACE REQUIREMENTS **46**

Chapter 1

INTRODUCTION

1.1. Overview. The WSS portfolio encompasses the management and execution of funding to sustain operationally accepted weapon systems by one USSF process owner through the Planning, Programming, Budgeting, and Execution (PPBE) process. This publication details the processes, roles, and responsibilities associated with WSS and is not meant to be all inclusive; additional details to execute external processes may be found in other publications referenced in **Attachment 1**.

1.2. Applicability. This SPFMAN applies to all program managers (PMs) and Field Commands (FLDCOMs) utilizing WSS-associated funding or involved in sustainment requirements determination. USSF utilizes the United States Air Force Centralized Asset Management database tool and associated schedules, managing their own requirements validation and funds execution processes. WSS processes provide service-level enterprise management with a focus of resources on USSF priorities.

1.3. Scope. The management of space weapon systems throughout their lifecycle involves a multi-functional, collaborative effort between the requirements, acquisition and sustainment, test, information operations, and intelligence communities. WSS is a subset of Readiness and Operation and Support funding, per DAFI 63-101/20-101, which is captured within four business process areas: depot purchased equipment maintenance (DPEM), contractor logistics support (CLS), sustaining engineering (SE), and technical orders (TOs).

1.3.1. DPEM involves maintenance and repair requiring overhaul, upgrading, or rebuilding of parts, assemblies, subassemblies, and software. The DPEM business process includes software maintenance and other major end items (OMEI) sub-categories.

1.3.2. CLS involves the performance of maintenance and/or materiel management functions for weapon systems by a commercial activity. The CLS business process includes CLS management support, CLS spares, CLS software, CLS OMEI, SE, training, and TOs sub-categories.

1.3.3. SE includes the identification, review, assessment, and resolution of deficiencies throughout a system's life cycle.

1.3.4. TOs include equipment technical manuals, engineering drawings, engineering data, and technical specifications required to support operations, maintenance, and repair.

1.4. WSS Governance. WSS governance processes are designed to internally prioritize WSS requirements, assess risks and impacts, administer strategic guidance, and formulate Service-level positions to execute WSS portfolio management. The WSS Executive Agent facilitates the WSS process through the approved governance structure on behalf of Deputy Chief of Space Operations for Operations (SF/S3/4/7). The Advisory Group (AG), Decision Board (DB), and Executive Council (EC) comprise the WSS governance structure.

1.4.1. The WSS governance structure ensures continuous process improvements are documented and implemented as required. The governance structure also manages WSS technical content, releases process data calls to all stakeholders, and participates in process collaboration and reviews. Voting membership is established at each level with chairs having final responsibility.

1.4.2. The frequency of WSS governance structure meetings is driven by major PPBE milestones, usually to develop risk-assessed positions in support of the Program Objective Memorandum (POM) and Execution Plan (ExPlan). Ad hoc or time sensitive issue resolution meetings can be called by the respective chair(s) at any time.


1.4.3. The AG is a working-level forum that reviews and elevates validated system requirements along with rationale and recommends potential tradeoffs, risks, and associated impacts to send forward to the DB. The AG is at the O-6/NH-04 (or equivalent) level. A list of the current AG chairs, advisors, and voting members is available from the Executive Agent upon request.

1.4.4. The DB vets and recommends Service-level system sustainment requirements, tradeoffs, risks, and impacts against space capability readiness requirements for final endorsement. At its conclusion, this board recommends an executable position on the WSS portfolio to the EC for final endorsement. The DB is at the General Officer/Senior Executive Service level and is chaired by the Associate SF/S3/4/7. A list of current DB advisors and voting members is available from the Executive Agent upon request.

1.4.5. The EC oversees all USSF governance matters providing strategic guidance, setting goals and priorities, and approving service-level positions for PPBE submissions into the Space Force Corporate Structure (SFCS). The EC is at the 3-Star/Senior Executive Service level and chaired by the SF/S3/4/7. Like voting membership, the EC has a board of directors consisting of Deputy Chief of Space Operations for Strategy, Plans, Programs, and Requirements (SF/S5/8); Deputy Assistant Secretary of the Air Force for Budget (SAF/FMB); Commander, Space Systems Command (SSC/CC); Commander, Combat Forces Command (CFC/CC); Commander, Space Training and Readiness Command (STARCOM/CC); Director, Science, Technology, Maturation, and Logistics Directorate (SAF/AQT); Director, Capability Delivery (SAF/SQS); and Portfolio Acquisition Executives (PAEs) with WSS equities. The board of directors advises the chair and offers expertise and recommendations for final decision. The SF/S3/4/7 (chair) is the final decision authority for WSS governance outputs and PPBE submissions.

1.5. WSS Process. The WSS process, as identified in **Figure 1.1** below, entails requirements definition and refinement, planning and programming, and budget and execution to provide DAF-wide visibility for WSS requirements.

Figure 1.1. The WSS Process.

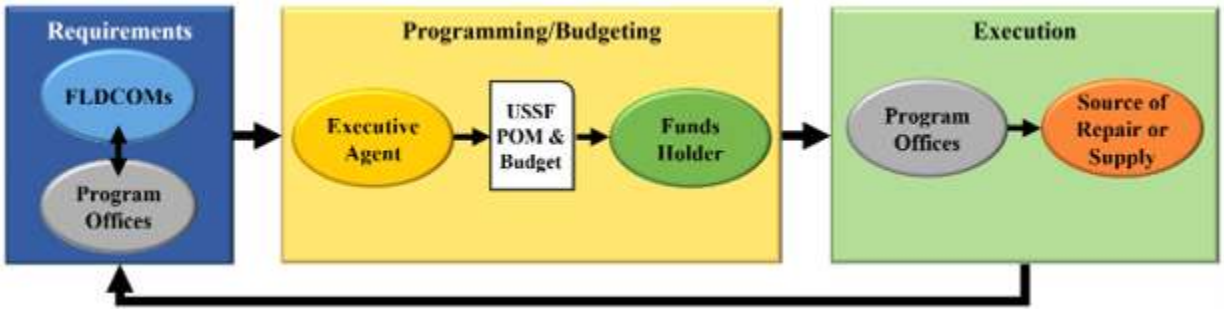

1.5.1. FLDCOMs and program offices must coordinate on weapon system sustainment requirements and program prioritization, and each program office will input sustainment requirements into the approved information technology (IT) system of record to provide requirements to the Executive Agent.

1.5.2. For the purpose of this publication, the program office role includes the PAE's functional sustainment teams (primarily led by Product Support Managers (PSMs)) within existing program offices, System Deltas, and/or Mission Delta Sustainment Squadrons, as applicable.

1.5.3. Requirements determinations and risk assessments are made jointly between the program offices/sustainment squadrons and their respective Delta leadership.

1.5.4. The program offices use guidance and direction to develop valid and defendable requirements. Stakeholders must collaborate on requirements during the Logistics Requirements Determination Process (LRDP) and publish validated requirements on or around 1 November of each year. The published requirements are provided to the Executive Agent for use in the development of the POM and ExPlan.

1.5.5. The Executive Agent works with the program offices and FLDCOMs to achieve a WSS governance-approved POM and ExPlan each year to be submitted to the SFCS. SFCS ensures an approved budget aligns with Strategic Defense Objectives and distributes dollars in each year of execution to the Executive Agent (e.g., Operating Agency Code (OAC) S7).

1.5.6. The Executive Agent distributes dollars to the program offices for execution.

1.5.7. Program offices send their dollars via funding documents to the approved source of repair (SOR) and source of supply providers which execute the dollars received.

1.5.8. DAF organic depot repair facilities reimburse the Air Force Working Capital Fund. Program offices pay for organic depot repair based on a bill of work with work hours multiplied by a depot rate, which the Air Force Sustainment Center Working Capital Fund establishes two years in advance.

1.5.9. Approved providers generally execute dollars directly and return excess funding to the program office to flow up to the Executive Agent.

1.6. Program Entry to WSS.

1.6.1. To be considered for entry into the WSS portfolio, the responsible PSM, on behalf of the PAE, must ensure the new program meets the entry criteria identified in the Program Entry to WSS Decision Tree (see **Attachment 2**), including a fully funded sustainment baseline which is detailed for emerging requirements in **Attachment 6**. **(T-1)**

1.6.2. Upon determining a program should be included into WSS, the PM completes and submits a "New Program Group, Program, or System Request Form" to the Executive Agent. The Executive Agent verifies validity of the form and coordinates the remaining signatures.

1.6.2.1. If the form inputs are not valid, the Executive Agent documents the rationale for form disapproval and provides the form back to the requesting PM to correct form shortcomings. The PM must revisit program entry criteria and form inputs to re-attempt program entry into the WSS portfolio.

1.6.2.2. The full routing of the form is approved by the Executive Agent before any new program group, program, or system is allowed to enter WSS. The "New Program Group, Program, or System Request Form" is available from the Executive Agent upon request.

Chapter 2

ROLES AND RESPONSIBILITIES

2.1. Assistant Secretary of the Air Force for Space Acquisition and Integration (SAF/SQ).

2.1.1. Participates as a voting member in WSS governance structure.

2.1.2. Responsible for coordination with Assistant Secretary of the Air Force for Acquisition, Technology, and Logistics (SAF/AQ) and the roles and activities detailed in Headquarters Air Force Mission Directive 1-17, *Assistant Secretary of the Air Force (Space Acquisition and Integration)*.

2.2. Deputy Chief of Space Operations for Operations (SF/S3/4/7).

2.2.1. Oversees WSS requirements and resourcing against readiness needs.

2.2.2. Authorizes and chairs the WSS governance structure as the approving body for WSS procedures and PPBE deliverables.

2.2.3. Authorizes WSS guidance, as coordinated through WSS governance.

2.2.4. Designates Mission Sustainment (SF/S4O) as SF/S3/4/7 lead for WSS guidance and resourcing.

2.2.5. Designates the WSS Executive Agent for enterprise portfolio management.

2.2.6. Mission Sustainment (SF/S4O).

2.2.6.1. Provides advocacy through SFCS forums.

2.2.6.2. Garners SF/S3/4/7 endorsement of service-level prioritized operational capabilities list.

2.2.6.3. Provides guidance for WSS portfolio processes.

2.2.6.4. Provides Budget Estimate Submission and President's Budget (PB) position to the Executive Agent.

2.2.6.5. Advocates for additional funds in support of emerging DAF priorities and informs the Executive Agent of impending force structure changes during the execution process.

2.2.6.6. Provides the deferral report to the Office of the Secretary of Defense (OSD).

2.2.6.7. Provides official WSS responses to Congressional and OSD requests for information.

2.2.6.8. Provides Budget Operations Directorate (SAF/FMBO) actuals submission after end of Fiscal Year (FY) for system of record.

2.2.7. Other SF/S3/4/7 3-letter organizations (L3).

2.2.7.1. Provides subject matter expertise in support of WSS governance structure.

2.2.7.2. Provides input on the service-level prioritized operational capabilities list.

2.2.7.3. Works with the Executive Agent on execution year emerging issues. May coordinate with external organizations with relevant subject matter expertise (e.g., SAF/FMB).

2.2.7.4. Provides impacts in regard to non-WSS Operation and Maintenance (O&M) operational requirements.

2.3. Deputy Chief of Space Operations for Strategy, Plans, Programs, and Requirements (SF/S5/8).

2.3.1. Provides strategic PPBE guidance in line with overall DAF strategy.

2.3.2. Advises WSS governance structure.

2.3.3. Plans and Programs Directorate (SF/S8P).

2.3.3.1. Advises the WSS governance structure on funding levels.

2.3.3.2. Provides programming assistance for WSS.

2.3.3.3. Advocates for resources during Program Budget Review deliberations.

2.3.3.4. Receives and consolidates USSF POM submissions.

2.4. Deputy Chief of Space Operations for Intelligence (SF/S2).

2.4.1. Provides guidance for and validates military intelligence programs.

2.4.2. Ensures intelligence, surveillance, and reconnaissance subject matter expertise is incorporated into the acquisition sustainment effort.

2.5. Field Commands (FLDCOMs): SSC, CFC, and STARCOM.

2.5.1. Responsible for coordinating collaboration with subordinate units.

2.5.2. Provide prioritized capabilities and impacts based on FLDCOM equities to SF/S3/4/7.

2.5.2.1. Conduct operational risk assessments and highlight impacts to warfighter capability.

2.5.2.2. Collaborate on acceptable risk levels for sustaining operational capability.

2.5.2.3. Collaborate on system acceptance criteria necessary to ensure sustaining systems, including permanent modifications, have the necessary resources required to support mission execution, per **Attachment 2**.

2.5.3. Participate in the WSS governance structure.

2.5.4. During the LRDP, FLDCOMs:

2.5.4.1. Collaborate on sustainment requirements and coordinate on prioritization impacts.

2.5.4.2. Assess requirements to maximize capability to the warfighter.

2.5.4.3. Assess and communicate updated or gap requirements to sustain desired level of capability.

2.5.4.4. Ensure all stakeholders are participating in the requirements collaboration phase to include collaborating on requirements according to established timelines.

2.5.5. During the POM process, FLDCOMs:

2.5.5.1. Assess risk category priorities within each assigned program group.

2.5.5.2. Assess allocated funding in the approved IT system of record to minimize risk and maximize capability to the warfighter.

2.5.5.3. Provide risk assessment impact statements at various funding scenarios.

2.5.5.4. Attend Executive Agent POM reviews to support risk assessment impacts.

2.5.6. During the ExPlan process, FLDCOMs:

2.5.6.1. Collaborate on strategic operations, reducing risk and maximizing readiness.

2.5.6.2. Collaborate with program offices on risk assessments and identifying unfunded requirements (UFRs).

2.5.6.3. Collaborate with program offices on identifying operational impacts made by requirement changes and/or funding adjustments.

2.5.7. During the execution year, FLDCOMs coordinate with program offices on execution year activities.

2.5.8. Appoint designee(s) and WSS functional assignments via email to the Executive Agent.

2.6. Portfolio Acquisition Executives.

2.6.1. Ensure assigned PSMs define, review, validate, and publish accurate, reliable, timely, and executable requirements.

2.6.2. Participate in the WSS governance structure.

2.7. Program Offices.

2.7.1. For the purpose of this publication, the program office role includes the Portfolio Acquisition Executive's functional sustainment teams (primarily led by Product Support Managers) within existing program offices, System Deltas, and/or Mission Delta Sustainment Squadrons, as applicable. Program office responsibilities described in this publication capture PM and PSM responsibilities, as the accountable program office leads, unless otherwise stated.

2.7.2. The PAE appoints PSM/PSM designee(s) and Program Group Requirements Manager assignments in writing and submits to the Executive Agent.

2.7.2.1. The PSM is accountable for all product support matters regarding program cost, schedule, performance, and supportability.

2.7.2.2. The PSM ensures the program's product support strategy integrates logistics, mishap data, intelligence supportability, and Environment, Safety, and Occupational Health risk data. The PSM also ensures the product support strategy includes integrated product support elements and aligns to overarching USSF enterprise priorities (see DAFI 63-101/20-101 for additional information).

2.7.3. During the LRDP, program offices:

2.7.3.1. Develop detailed requirements to meet desired capabilities and minimize risk while maximizing capability to the warfighter.

2.7.3.2. Develop and update detailed requirements to sustain desired level of capability.

2.7.3.3. Ensure all stakeholders are participating in the Requirements Collaboration phase.

2.7.3.4. Ensure all requirements with non-concur status are resolved prior to publishing requirements.

2.7.3.5. The PSM/PSM designee validates, prioritizes, and publishes requirements according to established timelines in conjunction with inputs from FLDCOMs.

2.7.4. During the POM process, program offices:

2.7.4.1. Establish risk category priorities and weights within each assigned program group. The PSM/PSM designee approves risk category priorities and weights.

2.7.4.2. Spread allocated funding in the approved IT system of record to minimize risk and maximize capability to the warfighter.

2.7.4.3. Provide impact statements at various funding scenarios.

2.7.4.4. Develop POM charts, and the PSM/PSM designee briefs each assigned program group to all stakeholders during the programmatic reviews.

2.7.4.5. Provide information to, and gather information from, FLDCOMs to support operational risk assessments.

2.7.5. During the ExPlan process, program offices:

2.7.5.1. Establish risk category priorities and weights within each assigned program group. The PSM/PSM designee approves risk category priorities and weights.

2.7.5.2. Collaborate with FLDCOMs on overall risk assessments and identifying UFRs.

2.7.5.3. Spread allocated funding to minimize risk and maximize capability to the warfighter in the approved IT system of record.

2.7.5.4. Collaborate with FLDCOMs on identifying operational impacts made by requirement changes and/or funding adjustments.

2.7.5.5. Develop program ExPlan charts, and the PSM/PSM designee briefs each assigned program group to all stakeholders.

2.7.6. During the execution year, program offices:

2.7.6.1. Manage program requirements and process requirement changes.

2.7.6.2. Manage funding, projected obligations, actual obligations, and contingent liabilities to identify UFRs in the approved IT system of record.

2.7.6.3. Coordinate with the Executive Agent on expired and cancelled year bills.

2.8. WSS Executive Agent.

2.8.1. CFC/S4 is the designated USSF Executive Agent for the WSS portfolio. The Executive Agent:

2.8.1.1. Provides enterprise-level oversight for WSS processes and the spread of funds against PAE-approved system-level requirements, in accordance with WSS governance direction. Serves as the integrator, facilitator, and continuous process improvement champion.

2.8.1.2. Manages the WSS portfolio through oversight and validation of logistics requirements utilizing approved, standard, and repeatable processes.

2.8.1.3. Manages and oversees the PPBE process deliverables for WSS requirements.

2.8.1.4. Engages with key stakeholders to ensure alignment of the USSF's most important sustainment needs with service objectives and priorities.

2.8.1.5. Ensures requirement change actions are reviewed, processed, and approved.

2.8.1.6. Validates final funding levels through WSS governance.

2.8.1.7. Coordinates on all policy, agreements, or procedures that impact WSS funding and commitments.

2.8.1.8. Complies with Headquarters Department of the Air Force (HQ DAF) taskings, policy, and guidance.

2.8.1.9. Coordinates all Cancelled Year invoices for WSS under OAC S7.

2.8.2. The Executive Agent acts as the requirements process owner of the WSS portfolio. As such, the Executive Agent:

2.8.2.1. Manages the WSS LRDP timeline, checklist, and kickoff training. Approves and validates data calls and integrates all stakeholder requirements.

2.8.2.2. Collaborates on and validates requirements.

2.8.2.3. Develops the WSS POM, including options, for submission to SF/S8P. Provides POM kickoff training to stakeholders, consolidates and integrates inputs, defends requirements, establishes funding targets, and approves and validates data calls. May coordinate with external organizations with relevant subject matter expertise (e.g., Air Force Materiel Command Product Support Management Division (AFMC/A4F)).

2.8.2.4. Provides direct assistance, oversight, and analysis to all stakeholders in developing and documenting WSS requirements and POM inputs.

2.8.2.5. Facilitates WSS governance meetings and validates final POM funding levels and risk through WSS governance.

2.8.2.6. Develops and manages the WSS POM chart template and training program.

2.8.2.7. Responsible for WSS equities within the approved IT systems of record.

2.8.2.8. Performs requirements analysis and reports metrics to stakeholders.

2.8.2.9. Validates requirement reconciliation and prepares deferral report.

2.8.2.10. Ensures program offices reconcile their obligations within the approved system of record.

2.8.2.11. During PPBE, sets desired risk levels and weighting of program groups within the portfolio based on service-level prioritized operational capabilities list.

2.8.3. The Executive Agent acts as the funds holder of the WSS portfolio. As such, the Executive Agent:

2.8.3.1. Manages funds according to existing approved requirements and based on USSF priorities and the mitigation solution for WSS UFRs.

2.8.3.2. Ensures available funding is provided to the highest priorities based on OSD, Secretary of the Air Force, and Chief of Space Operations guidance. This includes items such as projected need dates, program or mission risk, contract period of performance, system availability, prior year execution, response to natural disasters, impacts to readiness, and urgent requirements to prevent loss of life and/or assets.

2.8.3.3. Provides ExPlan kickoff and training to programs and FLDCOMs.

2.8.3.4. Distributes approved funding received from SAF/FMBO across weapon system requirements during each PPBE cycle.

2.8.3.5. Sets funding baseline for initial distribution in the execution year and facilitates and oversees program office funds spread throughout the execution year.

2.8.3.6. Ensures program offices reconcile their obligations monthly within the approved IT system of record.

2.8.3.7. Oversees funds distribution and balancing within the program groups.

2.8.3.8. Manages contingent liabilities.

2.8.3.9. Resolves shortfalls in the execution year utilizing the UFR process.

2.8.3.10. Coordinates with the program office points of contact in validating, prioritizing, and budgeting all requirements.

2.8.3.11. Collaborates on requirements and establishes funding levels for each program.

2.8.3.12. Performs initial funds spread in the approved IT system of record.

2.8.3.13. Coordinates and approves or disapproves requirement changes.

Chapter 3

LOGISTICS REQUIREMENTS DETERMINATION PROCESS (LRDP)

3.1. Overview. LRDP provides the process flow, as depicted in **Figure 3.1**, of the WSS requirements build for the POM process. LRDP is the annual process to create, validate, and defend WSS requirements. The Executive Agent provides the LRDP timeline for each POM cycle. LRDP requirements are divided into different risk categories, as defined in **Attachment 3**, and captured in the approved IT system of record. The applicable FLDCOM and the Executive Agent validate the requirements prior to PSM/PSM designee publishing. LRDP results will be used in the development of the POM, ExPlan, and weapon system analysis.

Figure 3.1. LRDP Process.



3.2. Phase One – Prepare Requirements. The program office, in conjunction with the FLDCOM, identifies new or emerging requirements and reviews existing requirements for currency in the approved IT system of record. Additional details on Emerging Space Requirements (ESR) can be found in **Attachment 6**.

3.3. Phase Two – Define Requirements. The PSM/PSM designee documents new or updates existing program requirements in the approved IT system of record and ensures requirements are documented in the appropriate risk category and Air Force Element of Expense Investment Code (AFEEIC). The program office evaluates each requirement based on anticipated programmatic changes, historical trends, programmed depot maintenance schedules, or any force structure changes provided by space staff through the Future Years Defense Program (FYDP).

3.4. Phase Three – Requirements Collaboration.

3.4.1. Identified weapon system stakeholders must review and collaborate on all requirements using the approved IT system of record.

3.4.2. Collaboration on each requirement provides stakeholder review and documentation of agreement or non-concurrence. The program office ensures all requirements with non-concur status, problems, or concerns are decided prior to moving into the next LRDP phase. If left unresolved, the requirement is at risk of not receiving funding during the POM cycle.

3.5. Phase Four – Prioritize Requirements. The program office, with input from the FLDCOMs, prioritizes individual requirements according to their relative importance in meeting USSF mission priorities and readiness standards.

3.6. Phase Five – Publish Requirements. Published requirements are due in accordance with the LRDP timeline issued by the Executive Agent. The PSM/PSM designee formally approves the validated requirements, within the approved IT system of record, as accurate, reliable, timely, and properly formatted via electronic signature, thus initiating the POM process.

3.7. General Requirements Management.

3.7.1. The Executive Agent provides training to include an LRDP reference guide to ensure that requirements across the WSS portfolio are consistent.

3.7.2. The program office reviews and documents requirements at an unclassified level, ensuring not to restate contract language when describing the requirement.

3.7.3. The program office ensures all requirement data elements are correct.

3.7.4. When describing the requirement, the program office addresses the following questions: who is doing the work (e.g., the name of the contractor or facility); what the requirement is funding; where, when, and how the work is accomplished. In addition, all new requirement descriptions include who approved the new workload, as well as the supporting decisional artifact (i.e., Air Force Form 1067, *Modification Proposal*, etc.).

3.7.5. When developing the requirement value, the program office details how the dollar value of each requirement is computed (e.g., quantity of hours, man-hours, units, locations, number of programmed depot maintenance, estimated unscheduled depot-level maintenance quantity, etc.).

3.7.5.1. The program office ensures the basis of estimate clearly defines the logic, method, data, and documented calculations used to estimate the resources required to perform the tasks. Some typical methodologies include historical program task and cost data, historical program or organizational productivity parametric data, firm quotation from a contractor or supplier, level of effort, or engineering estimate. The program office attaches supporting documentation to the requirement that shows how the requirement value was determined (e.g., a simplified independent cost estimate, like system, and original equipment manufacturer estimate).

3.7.5.2. If the historical or current FY obligation amount is significantly different than the requirement amount for the current POM year, the program office documents why there was a change to the requirement. If there is a reason using actual obligations is not sufficient for the current POM cycle requirement, the program office ensures documentation, including a cost estimate, is provided within the approved IT system of record.

3.7.5.3. Requirements for new programs or systems are captured in the ESR program group, as detailed in **Attachment 6**.

3.7.5.4. If there is a contract for the requirement, the program office ensures the contract value, or pre-negotiated option value, is used to determine the dollar value of the requirement and is captured as the contract cost. Contract information should be file maintained within the IT system of record to include, but not limited to, correct contract number, contract type, and period of performance.

3.7.5.4.1. A standard OSD inflation is added to requirements that do not utilize contract cost. Therefore, the PSM/PSM designee should not insert additional inflation into the requirement. If inflation is added into the requirement, the program office documents the rationale within the approved IT system of record.

3.7.5.4.2. Contracts should be written in a manner to provide flexible provisions that address a range of support requirements in order to accommodate changes in operational tempo or execution year funding, including surge or contingency requirements to the extent that they can be defined.

3.7.6. Variance Narratives.

3.7.6.1. When documenting variance narratives (i.e., historical execution variance, variance from the last year's LRDP requirement position to the current year's LRDP requirement, etc.), the program office ensures the variance statement explains the positive or negative dollar amount and the variance statement change(s) are documented in the approved IT system of record.

3.7.6.2. The program office documents what occurred within the program to cause the increase or decrease to the requirement within the approved IT system of record.

3.7.6.3. The program office provides programmatic impacts with reference to the change in quantities, man-hours, or other qualitative details to explain the variance.

3.7.7. Programmatic Success and Failure Points.

3.7.7.1. The success point is equal to the requirement for a given task and is defined as the point where there is zero programmatic risk for that task; the program achieves the ultimate goal or activity. Each requirement should have a success point which equals 100% of the requirement value.

3.7.7.2. The failure point is the funding level which would result in a significant impact to capacity or capability or the inability to meet sustainment metric goals. The current programmatic failure point definitions are defined in **Attachment 4**. The programmatic failure point definition is different for each of the risk categories. The program office ensures the failure point justification explains the rationale for how the failure point was determined and calculated.

3.7.8. A Requirement Control Number (RCN) is required for all organic workloads. A new RCN is required to be created when there is a change in workload type. The program office cannot reuse RCNs if there is a scope change on the task, as this can create issues when performing historical variances.

3.7.9. For changes in type of work, SOR, program group, or AFEEIC, the program office creates a new requirement.

3.7.10. Program Management Administration (PMA) costs are not valid WSS requirements, and thus the program office cannot create tasks in any category for PMA. However, certain Federally Funded Research and Development Centers, including University-Affiliated Research Centers, that are considered PMA and operating in a depot function are authorized to use WSS funding. Federally Funded Research and Development Centers and University-Affiliated Research Centers requesting WSS funding must contact the Executive Agent for clarification and approval. **(T-1)**

3.7.11. The task description must reflect the proper cost element structure code. Cost element structure codes are located within the Operations and Support Guide published by OSD.

3.7.12. The official definitions of AFEEIC attributes are located within the Financial Management Data Quality Service at **https://fmdqs.cce.af.mil/saml/home.htm**.

3.7.13. If the work does not clearly fit in a defined AFEEIC, the program office must request assistance from the Executive Agent in classifying the work under the most appropriate AFEEIC and provide supporting documentation. **(T-1)**

Chapter 4

PROGRAM OBJECTIVE MEMORANDUM (POM) PROCESS


4.1. Overview. The WSS POM details the planned funding of WSS requirements and the corresponding programmatic risk to the WSS portfolio through the FYDP. The Executive Agent completes this task utilizing USSF priorities, risk modeling, planned force structure changes, and resource changes to develop the recommended WSS budget and submits it to WSS governance structure for approval. Documentation of requirements, funding, and risk is accomplished in the approved IT system of record. The Executive Agent provides the POM timeline for each POM cycle.

4.1.1. The governance-approved WSS POM is submitted to SF/S8P for SFCS deliberations.

4.1.2. The WSS POM process provides necessary inputs used in planning future organic depot maintenance workload resources. For USSF-resourced workloads at DAF air logistics complexes, the WSS POM process provides a workload file that is one of the three inputs into the Requirements Review and Depot Determination process.

4.1.3. There are four phases to building the POM: Preparation; Development; Review, Validation, and Adjustment; and Approval. **Figure 4.1** documents stakeholders, inputs and major actions, and the approval process.

Figure 4.1. POM Phases.

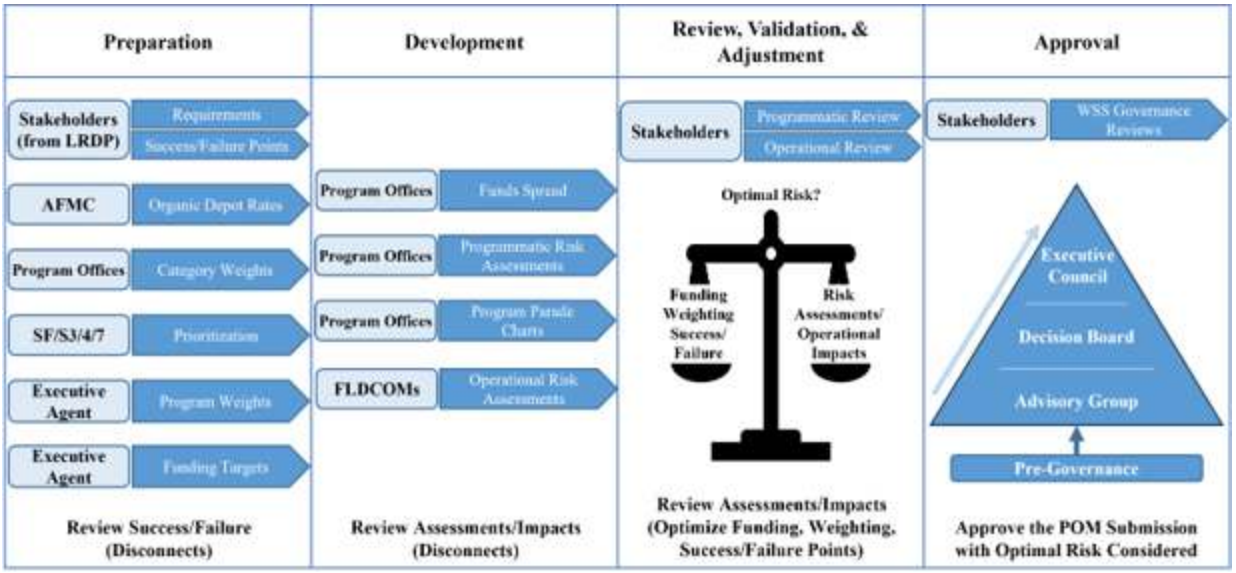

4.2. Phase One – Preparation.

4.2.1. The preparation phase consists of using the latest published WSS requirements based on service-level prioritization endorsed by SF/S3/4/7, and associated pricing from base year (BY) to then-year dollars, utilizing both the organic depot rates provided by Air Force Materiel Command and Department of Defense standard inflation factor. In addition, risk category weights and program weights are developed to support risk modeling. The Executive Agent uses the accumulation of this information to establish funding targets for each program. Documentation of requirements and funding is accomplished in the approved IT system of record.

4.2.2. POM development begins with the latest LRDP published WSS requirements in BY dollars. BY is the FY value utilized across the FYDP. For example, FY23 values are used to price out the FY24 through FY30 requirements, for use in the FY25 POM and FY24 ExPlan. Program offices may need to adjust requirements based on USSF planned force structure changes.

4.2.3. Current organic depot rates and factors, plus designated current inflation values, are used to price out the BY requirement values into then-year dollars (e.g., FY25 POM, FY24 ExPlan, and any other financial drills required) using the WSS LRDP requirements.

4.2.4. Success and failure points published during the LRDP are utilized in the risk model.

4.2.5. Program offices, in collaboration with the Executive Agent, must establish risk category weights for their respective program groups. **(T-1)** Program weighting reflects the relative proportional importance or criticality to the overall mission at the risk category level. A higher weighted risk category will indicate higher importance or criticality to the mission and therefore less willingness by the program office to assume risk in WSS funding for that risk category. Each requirement is associated with an AFEEIC, which is tied to a risk category and contributes to a program's overall risk rating.

4.2.6. SF/S4O coordinates service-level prioritization of the program groups with the WSS Enterprise, garners SF/S3/4/7 endorsement, and distributes the final product for POM development activities.

4.2.7. The Executive Agent provides weighting of program groups in accordance with the service-level prioritization.

4.2.8. Utilizing USSF priorities, risk modeling, POM technical guidance, and approved force structure changes, the Executive Agent establishes funding targets for each program group in their OAC within the funding targets and guidance provided by space staff.

4.3. Phase Two – Development.

4.3.1. During the development phase, the program office spreads the funding targets provided by the Executive Agent, assesses program risk, and builds the program POM charts. Documentation of requirements and funding is accomplished in the approved IT system of record.

4.3.2. Although not required, program offices have the opportunity to realign funding within the funding target during this phase. Realignment should optimize the program's funding and reduce program risk. The program office uses the risk model assessment generated from the approved IT system of record to provide programmatic risk assessments.

4.3.3. The Executive Agent provides the POM chart template and training. The program office develops POM charts within the approved IT system of record, meets established timelines, and presents their charts during governance meetings. FLDCOMs must provide an operational risk assessment and associated operational impact statements based on the data provided by the program office, which are to be included in the program charts. **(T-1)**

4.4. Phase Three – Review, Validation, and Adjustment.

4.4.1. During the review, validation, and adjustment phase, WSS holds programmatic reviews to give the PSM/PSM designee an opportunity to brief program risk based on projected funding for the POM year.

4.4.1.1. All programs will be scheduled for a programmatic review unless directed otherwise by the Executive Agent. The Executive Agent provides a schedule for all programs participating.

4.4.1.2. During the programmatic review, the PSM/PSM designee will brief program risk and advocate for additional funds if required. They may also identify excess funds or any mitigation plans. **(T-1)**

4.4.1.3. The PSM/PSM designee and all primary stakeholders must participate in the discussion during the programmatic review. **(T-1)**

4.4.1.4. The PSM documents any changes from the programmatic review in the approved IT system of record.

4.4.2. An operational review is held for all programs to communicate operational risk based on impacts identified during operational risk assessments.

4.4.2.1. The FLDCOMs must identify and assess operational risks based on resourcing levels determined during the programmatic review. **(T-1)**

4.4.2.2. During the operational review, FLDCOMs must brief operational risk, identify any mitigation plans, and provide a narrative for resource advocacy. **(T-1)**

4.4.2.3. FLDCOMs and all primary stakeholders must participate in the discussion during the operational review. **(T-1)**

4.4.3. Primary stakeholders for this phase are PSMs; FLDCOMs; the Executive Agent; SF/S4O; SF/S8P; and SAF/SQS, with relevant input from external organizations (e.g., SAF/FMB and SAF/AQD). Dependent on program priority or special interest, other participants may attend the programmatic review and/or operational review.

4.5. Phase Four – Approval.

4.5.1. During the approval phase, the Executive Agent consolidates the WSS POM recommended position based on the programmatic review and operational review results and presents to the WSS governance structure for approval to submit to SFCS.

4.5.1.1. Stakeholders will participate in WSS governance as outlined in **paragraph 1.4**. **(T-1)**

4.5.1.2. The Executive Agent facilitates all three tiers of the WSS governance meetings and coordinates across the Enterprise to schedule the meetings and provide read-ahead slides to stakeholders.

4.5.2. The Executive Agent documents any changes from the WSS governance with respect to requirement value, success or failure point, or funding signs in the approved IT system of record.

4.5.3. Once changes have been completed and updated, the Executive Agent submits the final product to SFCS for senior leader decision making processes.

Chapter 5


EXECUTION PLAN (EXPLAN) PROCESS

5.1. Overview. The ExPlan details the planned funding and corresponding risk to requirements for the upcoming FY.

5.1.1. The Executive Agent completes this task each cycle for the WSS budget as a service-level position and submits the WSS governance-approved position to SAF/FMBO.

5.1.2. The four phases to building the ExPlan are: Preparation; Development; Review, Validation, and Adjustment; and Approval. **Figure 5.1** documents stakeholders, inputs and major actions, and the approval process.

Figure 5.1. ExPlan Process.

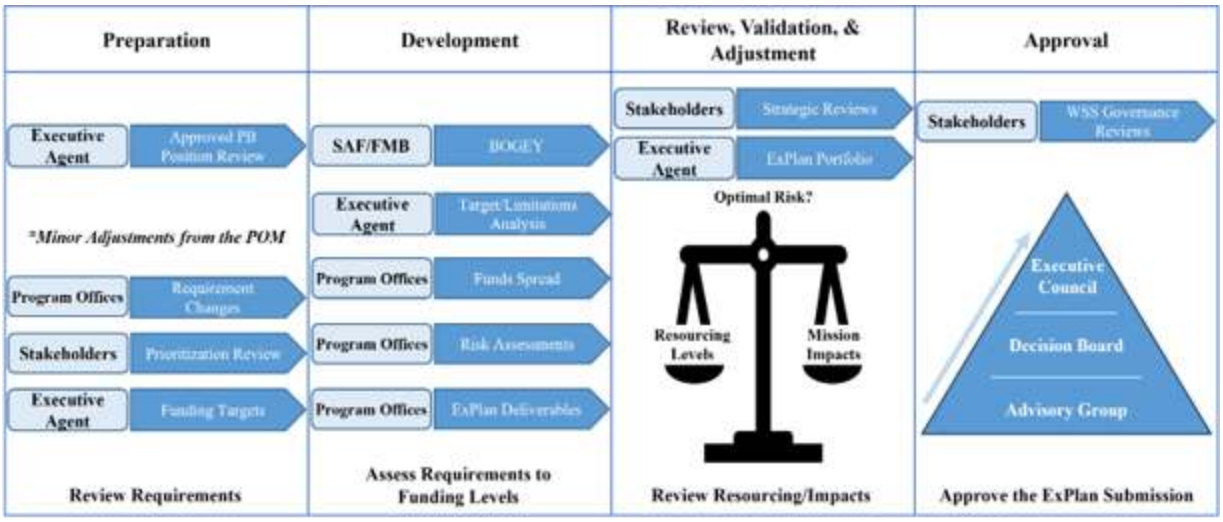

5.2. Phase One – Preparation.

5.2.1. The starting point for the ExPlan utilizes the approved PB position for WSS requirements for each program, updated by the recently vetted POM process, as a result of adjustments to success and failure points, organic depot rates, risk category weights, prioritization, and program weights.

5.2.1.1. Requirement changes during ExPlan are limited to fact-of-life changes (e.g., new contract award) or fluctuations due to factors outside the control of the program office (e.g., organic labor rate adjustments) which have a significant dollar change to the program. The Executive Agent will provide guidance and approval for making requirement changes during the ExPlan.

5.2.1.2. Additional funding for new or adjusted requirements above the approved PB position is not guaranteed.

5.2.2. Prioritization Review. Stakeholders must review program prioritization, based on continual threat assessment, and provide an updated prioritization list, if required, to the Executive Agent. **(T-1)**

5.2.3. Funding Targets. The Executive Agent sets initial funding targets based on the current approved funding level to minimize risk. The funding targets contain the initial breakout of the funding by financial limitations (e.g., sub-activity group, military intelligence program, other limitations, etc.).

5.3. Phase Two – Development.

5.3.1. The Executive Agent utilizes the success and failure points and weighting to complete the spread of funding.

5.3.2. Budget Outlay Governing Execution Year (BOGEY). The Executive Agent develops the ExPlan using the SAF/FMB-issued initial BOGEY.

5.3.3. Target and Limitation Analysis. The Executive Agent analyzes the initial BOGEY file and realigns funds to best minimize risk across the portfolio while adhering to fiscal limitations.

5.3.4. Program Office Funds Spread and Risk Assessments. The program office reviews the initial funds spread and has the opportunity to re-spread funds to more accurately align with mission requirements, within limitations. Program offices, in conjunction with FLDCOMs, must provide an overall risk assessment based on the funding level and determine justification for any requirements beyond the BOGEY to identify UFRs. **(T-1)**

5.3.4.1. All UFRs are categorized using definitions provided by SAF/FMB and the Executive Agent. Additional funding for UFRs is not guaranteed.

5.3.4.2. Program offices, in coordination with FLDCOMs, will identify impacts made by requirement changes and/or funding adjustments. **(T-1)**

5.3.5. ExPlan Chart Submission. The Executive Agent may request additional information from program offices in the ExPlan deliverables to help determine where to best realign funding during strategic reviews. Requested deliverables give programs the opportunity to highlight major issues and programmatic and operational impacts on the overall health of the WSS portion of the program due to UFRs. The ExPlan charts gives decision makers an overall program health assessment for the upcoming FY.

5.4. Phase Three – Review, Validation, and Adjustment.

5.4.1. During this phase, the funds spread and risk assessments that were completed in the first two phases are used to evaluate the risk levels of the programs.

5.4.2. Strategic Reviews. The Executive Agent organizes strategic reviews to provide stakeholders with the results of the funds spread and the risk assessments for each program and facilitates discussions to vet the recommended allocation of funding across the WSS portfolio to maximize warfighter capability and minimize risk.

5.4.2.1. The ExPlan charts are reviewed during the strategic reviews. The charts are forwarded to SAF/FMBO for further consideration by DAF.

5.4.2.2. The Executive Agent reviews operational impacts during strategic reviews and coordinates with program offices and FLDCOMs if more information is required.

5.4.3. ExPlan Portfolio. The Executive Agent consolidates and finalizes the outcome of the strategic reviews into the service-level ExPlan position.

5.5. Phase Four – Approval. The final phase of the ExPlan process involves submission of the recommended ExPlan, along with collaborative risk assessments through the WSS governance structure. The EC provides final approval of the WSS ExPlan, and the Executive Agent submits to Assistant Secretary of the Air Force, Financial Management and Comptroller (SAF/FM) in accordance with SAF/FM's approved process.

5.6. Post-approval Activities. Once the EC approves the ExPlan, the Executive Agent tasks the program offices to provide a monthly obligation forecast by requirement in the approved IT system of record, which then forms the baseline obligation forecast for the upcoming FY.

Chapter 6

EXECUTION PROCESS

6.1. Overview. In the year of execution, the Executive Agent oversees execution of all funding budgeted for WSS requirements.

6.1.1. The Executive Agent monitors, manages, and reports on the Congressional fiscal limitations set forth in the annual Defense Appropriations Act.

6.1.2. Based on specific guidance and direction received from HQ DAF each FY, the Executive Agent issues updated execution year guidance for WSS. Execution year activities begin on 1 October and end 30 September each FY in accordance with **Figure 6.1** below.

Figure 6.1. Execution Activities Timeline.



* A Continuing Resolution's (CR) impact on the activities is considered in this timeline. The timeline may shift if there is no CR in a fiscal year.

6.2. Weapon System Sustainment Requirements.

6.2.1. The program office must ensure the requirements are current, executable, and maintained in the approved IT system of record to reflect mission needs. **(T-1)**

6.2.2. The program office must update any current year requirements to show a requirement change in the IT system of record. The program office will make necessary adjustments to any current year requirements that were deferred from a previous year or funded as a buy down in the previous FY. **(T-1)**

6.2.3. The program office must follow the process documented in **paragraph 6.5** for any requirement changes. **(T-1)**

6.2.4. Monthly Obligations. The program office must ensure the requirement funding values in the approved IT system of record match the end-of-month position in the official accounting systems no later than the fifth business day of the month. **(T-1)** This includes approved funding, obligations, processing requirement changes, and updating the UFRs list.

6.2.5. End-of-Year Obligations. The program office must ensure the requirement funding values in the approved IT system of record match the end-of-year position in the official accounting systems no later than the fifth business day after the end of the FY. **(T-1)** This includes approved funding, obligations, and contingent liabilities.

6.3. Funding.

6.3.1. For WSS requirements, the Executive Agent distributes funding based on Congressional language and HQ DAF execution guidance priorities.

6.3.2. The program office must update all funding realignments, additional funding requests, and identification of excess funding in the approved IT system of record no later than the fifth business day of the month. **(T-1)**

6.3.3. The Executive Agent's overarching FY execution guidance includes major activities that impact WSS execution and funding at the program office, FLDCOM, and portfolio level. Different processes will be outlined in the FY execution guidance for managing and allocating funds during the following:

6.3.3.1. Continuing Resolution. Minimal funding is required to continue operations until a budget is passed.

6.3.3.2. Initial Distribution. Annual authority is provided to programs aligned with the current ExPlan. Any Congressional marks or directives could potentially impact the annual authority allotted during the ExPlan.

6.3.3.3. UFR List. The UFR list outlines prioritization of remaining unfunded and executable requirements in preparation for annual close out. Emergent UFRs not on the current WSS consolidated UFR list that are brought forward during the last two months of the FY will be managed on a case-by-case basis.

6.3.3.3.1. The program office, in coordination with FLDCOMs, must determine prioritization across their portfolio and submit their UFR list to the Executive Agent. **(T-1)**

6.3.3.3.2. The Executive Agent creates a consolidated list of UFRs from program office submissions in alignment with service-level priorities.

6.3.3.4. Mid-Year Reviews. The reviews track weapon system funds execution to forecast, identifies excess funding and UFRs, and highlights canceled year funding and major program concerns.

6.3.3.4.1. Mid-Year Reviews evaluate overall portfolio progress meeting statutory limitations of the 80/20 rule (i.e., no more than 20% of one-year appropriations may be obligated during the last two months of the FY).

6.3.3.4.2. All funding documents must be processed and in the accounting system by 31 July each FY. All uncommitted funds will be returned to the WSS portfolio, placed in the withhold account, and be used for approved items on the UFR list.

6.3.3.5. Future ExPlan. The future FY ExPlan details the planned funding and corresponding risk to requirements for the upcoming FY with the intent to balance operational needs with funding.

6.3.3.6. Close out. Actions include the management and redistribution of remaining unobligated balances for obligation by 30 September each FY.

6.4. Forecast and Actual Obligation Updates.

6.4.1. The program office must update actual and projected monthly obligations for WSS requirements in the approved IT system of record at the RCN (requirement) level no later than the fifth business day of the month. **(T-1)** Stakeholders rely on this data to respond to execution year taskers and real-time decisions. These updates provide historical execution for each requirement, which is used for justification of requirements and failure points for future POM cycles.

6.4.2. Upon approval of upward obligation authority by the Executive Agent, requirement and funding values will be updated in the applicable FY's version of the approved IT system of record. This may cause a requirement change that needs to be processed.

6.4.3. The program office identifies deferrals by following the requirement change process documented below to support deferral reporting. The Executive Agent is required to provide SF/S4O the projected deferral report mid-FY and final deferral report at FY end.

6.5. Requirement Changes.

6.5.1. Requirement changes are documented to capture changes in the current execution year for either new requirements not previously documented in the approved IT system of record or existing requirements within the approved IT system of record. The requirement change process is used to identify, validate, coordinate, document, amend, and approve changes to WSS requirements outside the normal requirements determination cycle.

6.5.2. The Executive Agent has established thresholds in the approved IT system of record that determine whether the requirement change is automatically approved or requires processing for approval. See **Attachment 5** for the current approval threshold by requirement change type.

6.5.3. No obligations are authorized until the requirement change has been completely approved at all levels within the approved IT system of record.

6.5.4. Requirement Change Process.

6.5.4.1. The program office initiates the requirement change process as soon as a change is identified.

6.5.4.2. The program office coordinates the requirement change through the necessary approval chain within five business days of process initiation.

6.5.4.3. When accomplishing a requirement change for organic depot workload, the program office attaches concurrence documentation, such as an email, from the Air Logistics Complex Business Office to validate agreement for the change.

6.5.4.4. The program office provides the correct requirement change type, funding need by date, requirements the funds will be moved to or from, requirement change justification, source of funding, requirement description, mission impact, and whether the requirement change is unfunded or not.

6.5.4.5. The Executive Agent reviews the requirement change submission for approval or disapproval. If the requirement change is disapproved, the program office should mitigate the issue(s) and resubmit.

6.5.4.6. The Executive Agent uses the requirement change-type deferral to provide SF/S4O the projected deferral report at mid FY and final deferral report at FY end.

6.5.4.7. Requirement Change Types and Definitions:

6.5.4.7.1. Buy Down. The requirement for the current execution year did not change but is being increased to buy down future work. This will apply existing funds for requirements planned in future years. Buy downs will always be increases to current year requirements and decrease future year or next FY requirements.

6.5.4.7.2. Prior Buy Down. The offsetting requirement change type for a requirement that was bought down in the previous FY. This will always be a requirement decrease and should not exceed the amount or quantity bought down in the previous FY.

6.5.4.7.3. Price Change. The volume of work or scope of the requirement did not change, but the price changed due to negotiated contract values, labor rate adjustments, or newly awarded contracts.

6.5.4.7.4. Scope Change. The volume of existing work increased or decreased.

6.5.4.7.5. Unpublished Requirement. Any task or requirement that is brand new, had been previously archived or published as zero dollars, or was published with a different AFEEIC.

6.5.4.7.6. Deferral. The requirement is valid but not accomplished during execution year, shifting existing requirements into future year(s). This type of requirement change will always be a requirement decrease in execution year and generate a prior deferral requirement change in future year(s).

6.5.4.7.7. Prior Deferral. The offsetting requirement change type for a requirement that was previously deferred in a prior FY. This will always be a requirement increase and should not exceed the amount or quantity deferred in a previous FY.

6.5.4.7.8. Unexecutable. This represents a valid requirement that could not be executed due to funding restraints, schedule changes, etc. and resulted in a missed opportunity in the year of execution. This requirement will not defer to another year and will always be a decrease to the requirement.

6.6. Unfunded Requirement Requests.

6.6.1. The prioritized ExPlan UFR list is carried over as the starting point in the year of execution. Program offices must submit new UFRs to the Executive Agent for consideration in the existing UFR list. **(T-1)** Procedures may be adapted in the year of execution due to additional guidance.

6.6.2. The program office, in conjunction with the applicable stakeholders, must review requirements to determine if internal adjustments to existing funding can satisfy the UFR. **(T-1)** This review should include analysis of prior year deferrals. If WSS funding for a UFR is no longer required, the program office must notify the Executive Agent within 10 business days. **(T-1)**

6.6.3. If the funding disparity cannot be resolved at the program office level, the program office seeks Executive Agent guidance to realign funding within their WSS portfolio.

6.6.4. At a minimum, the UFR request should document the requirement that funds are being requested for and the operational and programmatic impacts of funding the addition to the requirement. If a UFR request increases a current requirement, it must have an approved requirement change.

KATHRYN L. KOLBE, SES
Deputy SF/S3/4/7, Installations & Logistics, USSF

Attachment 1

GLOSSARY OF REFERENCES AND SUPPORTING INFORMATION

References

DAFI 63-101/20-101, *Integrated Life Cycle Management*, 16 February 2024

DAFMAN 90-161, *Publishing Processes and Procedures*, 18 October 2024

DAFMAN 63-122, *Depot Source of Repair Planning and Activation*, 27 September 2024

DAFMAN 65-605, *Vol. 1, Budget Guidance and Technical Procedures*, 31 March 2021

HAFMD 1-17, *Assistant Secretary of the Air Force (Space Acquisition and Integration)*, 30 September 2022

AFI 33-322, *Records Management and Information Governance Program*, 23 March 2020

SPFI 13-604, *System Acceptance*, 30 August 2023

TO 00-05-01, *Air Force Technical Order System*, 1 October 2014

TO 00-05-03, *Air Force Technical Order Life Cycle Management*, 15 February 2019

TO 00-05-15, *Air Force Time Compliance Technical Order Process*, 15 May 2014

TO 00-25-108, *Communications-Electronics (C-E) Depot Support*, 7 August 2012

Prescribed Forms

None

Adopted Forms

AF Form 1067, *Modification Proposal*

DAF Form 847, *Recommendation for Change of Publication*

Abbreviations and Acronyms

AFEEIC—AF Element of Expense Investment Code

AG—Advisory Group

BOGEY—Budget Outlay Governing Execution Year

BY—Base Year

CFC—Combat Forces Command

CLS—Contractor Logistics Support

DAF—Department of the Air Force

DAFI—Department of the Air Force Instruction

DB—Decision Board

DPEM—Depot Purchased Equipment Maintenance

DSOR—Depot Source of Repair

EC—Executive Council

ESR—Emerging Space Requirements

ExPlan—Execution Plan

FLDCOM—Field Command

FYDP—Future Years Defense Program

FY—Fiscal Year

HQ DAF—Headquarters Department of the Air Force

IT—Information Technology

KPP—Key Performance Parameter

KSA—Key System Attribute

LCSP—Life Cycle Sustainment Plan

LRDP—Logistics Requirements Determination Process

O&M—Operation and Maintenance

OA—Operational Acceptance

OAC—Operating Agency Code

OMEI—Other Major End Item

OPR—Office of Primary Responsibility

OSD—Office of the Secretary of Defense

PAE—Portfolio Acquisition Executive

PB—President's Budget

PM—Program Manager

PMA—Program Management Administration

POM—Program Objective Memorandum

PPBE—Planning, Programming, Budgeting, and Execution

PSM—Product Support Manager

RCN—Requirement Control Number

RGC—Repair Group Category

SAF—Secretary of the Air Force

SE—Sustaining Engineering

SFCS—Space Force Corporate Structure

SOR—Source of Repair

SORA—Source of Repair Assignment

SSC—Space Systems Command

STARCOM—Space Training and Readiness Command

TO—Technical Order

UFR—Unfunded Requirement

USSF—United States Space Force

WSS—Weapon System Sustainment

ZBT—Zero-based Transfer

Office Symbols

AFMC/A4F—Air Force Materiel Command Product Support Management Division

CFC/CC—Commander, CFC

SAF/AQ—Assistant Secretary of the Air Force for Acquisition, Technology, and Logistics

SAF/AQT—Director, Science, Technology, Maturation, and Logistics Directorate

SAF/FM—Assistant Secretary of the Air Force, Financial Management and Comptroller

SAF/FMB—Deputy Assistant Secretary of the Air Force for Budget

SAF/FMBO—Budget Operations Directorate

SAF/SQ—Assistant Secretary of the Air Force for Space Acquisition and Integration

SAF/SQS—Director, Capability Delivery

SF/S2—Deputy Chief of Space Operations for Intelligence

SF/S3/4/7—Deputy Chief of Space Operations for Operations

SF/S4O—Mission Sustainment

SF/S5/8—Deputy Chief of Space Operations for Strategy, Plans, Programs, and Requirements

SF/S8P—Plans and Programs Directorate

SSC/CC—Commander, SSC

STARCOM/CC—Commander, STARCOM

Terms

Approved—Formal sanction by PM or recognized authority.

Base Year—A reference period which determines a fixed price level for comparison in economic escalation calculations and cost estimates. The price level index for the base year is 1.000.

Budget Outlay Governing Execution Year—The estimate of what will eventually be in the appropriation bill passed by Congress. After the bill is passed, dollars are issued to the Office of the Secretary of Defense to apportion to the Service. The Service allocates to organizations to execute dollars against their specific requirements to meet mission intent and need as requested during the budgeting process to include the POM and ExPlan.

Buy Down—The requirement for the current execution year did not change but is being increased to buy down future work. This will apply existing funds for requirements planned in future years. Buy downs will always be increases to current year requirements and decrease future year or next FY requirement.

Canceled Year Funding—Funding that is no longer available for obligation or expenditure for any purpose.

Close Out—Documentation and reconciliation of all activities involved with a contractor's completion of overall tasks.

Commodity—A segmented category of goods or services. The Executive Agent utilizes AFEEICs to establish WSS commodities.

Contractor Logistics Support (CLS)—A method of contract support for a program, system, subsystem, training system, equipment, or end item used to provide all or part of the sustainment elements in direct support of the approved sustainment strategy. It may include work managed or accomplished by the Government but where contractors are responsible for performance output.

Deferral Report—A report of valid requirements that are not accomplished during execution year, shifting the requirements into future year(s). Available budgetary resources are withheld from obligation or expenditure temporarily for the list of deferred requirements.

Define Requirements—Program offices identify and update all program requirements within the approved IT system of record. Program requirements include force structure changes, operational tempo, historical trends, programmed depot maintenance schedules, and any other major programmatic changes through the FYDP, as provided by HQ DAF and FLDCOMs.

Depot Maintenance—Material, software maintenance, or repair requiring the overhaul, upgrade, or rebuild of parts, assemblies, subassemblies, or software programs, regardless of source of funds, location, or if accomplished organically or commercially. The term does not include procurement of modifications for performance improvement. It does include testing, installation of parts for modifications, and reclamation of materiel. Reference Title 10, United States Code, Section 2460.

Depot Purchased Equipment Maintenance (DPEM)—Covers the method for procuring depot maintenance services from organic or contractor depot maintenance resources. This involves customer management to determine requirements, obtaining financial Obligation Authority, and providing programming authority for ordering work from depot maintenance.

Executable—Individual tasks logistically supportable for the year(s) requested.

Execution Year—The year in which there is a bona fide need. Program offices seek funds in the execution year's budget to finance the need. This funding is in then-year dollars.

Financial Management Data Quality Service—The Financial Management Data Quality Service is the Authoritative Data Source for Space Force financial programming, execution, reporting data element code values, titles, descriptions, and period of availability. Access at the following website: **https://fmdqs.cce.af.mil/saml/home.htm**.

File Maintain—The physical act of entering or updating data in the approved IT system of record.

Funds Holder—The organization with authority to commit funds and issue a project order or other funding document directing depot maintenance to perform a repair action. The Executive Agent acts in the funds holder capacity for the WSS Portfolio.

Legacy—For the purpose of this publication, an existing program, system, or program group that has been fielded and funded by the WSS portfolio.

Logistics Requirements Determination Process (LRDP)—Simplified, standard, repeatable, and consistent process to determine and prioritize weapon system requirements across the entire USSF to optimally sustain weapon systems within requisite resource constraints.

LRDP Timeline—A calendar year schedule providing due dates for the major phases of the LRDP. The LRDP timeline will be distributed annually by means of slides, emails, and through the approved IT system of record to the start of the process.

Modification—A change in form, fit, or function to a system component, end item, piece of equipment, or software that affects the performance, ability to perform the intended mission, production, or maintenance. Such modifications are generally accomplished to add a new capability or function to a system or component, or to enhance the existing technical performance or operational effectiveness of the asset.

OAC S7—The operating agency code for the USSF WSS portfolio used for accounting purposes. Operating agency code is defined as the two-position alphanumeric code for a major high-level organizational unit within the Department of the Air Force to which funds are allocated.

Organic—Logistics support provided by Government-owned material, equipment, or facilities and Government personnel.

Organic Depot—Depot maintenance facility where actions are performed by a military service under military control using Government-owned or controlled facilities, tools, test equipment, spares, repair parts, and military or Government civilian personnel.

Organizational Productivity Parametric Data—A statistics-based methodology to calculate the expected amount of financial resources or time that is required to perform and complete a project, ultimately used in determining an estimate of requirement value.

Planning, Programming, Budgeting, and Execution (PPBE)—The PPBE process consists of two major programming and budgeting exercises, the President's baseline review and the President's Budget (PB). It is a continuous cycle with the PPBE segments in any given year overlapping segments of a number of other years. Programming links mission requirements to the financial resources required. The result of this linkage is that resources can be allocated in a systematic way with a direct relationship to the roles and missions of DAF and Department of Defense (or DD when referring to forms). The process also provides the information USSF senior

leaders need to balance all the Service's fiscal needs. Requirements are first identified in the POM, the first phase of the PPBE. It is the place to bring forward all requirements to be funded across the FYDP so the USSF can identify funds needed to accomplish the work. The POM forecasts USSF requirements five to six years into the future to accomplish long-term planning and secure funding. The PB ultimately results in funding authorized and appropriated by Congress to USSF for the execution year.

Prepare Requirements—Identify new emerging requirements and validate existing requirements.

Prioritize Requirements—Once validated, the program office, in coordination with FLDCOMs and supported commands, will sort requirements according to their relative importance in meeting USSF priorities (weapon system availability, capability, etc.).

Portfolio Acquisition Executive—The senior acquisition official designated by the Service Acquisition Executive to lead a portfolio of capabilities, with authority for plans, budgets, and execution of programs assigned to the portfolio, including life-cycle management. PAEs are also responsible for developing and approving system-level requirements within their respective portfolio.

Product Support Manager—The PAE-designated individual responsible for managing product support required to field and maintain the readiness and operational capability of a system throughout the life cycle.

Program Group—A WSS term that is used throughout the WSS process. In most cases the program group is synonymous with a weapon system PM. All WSS requirements are grouped into specific program groups with each having a PM, typically an O-6/NH-04 (or equivalent), who validates and publishes those requirements annually.

Program Management Administration (PMA)—PMA is a cost which supports the operation of a PSM/PSM designee in their management and oversight role and is not a valid WSS requirement. PMA includes costs such as program office travel, office printing, supplies, equipment, PSM-unique computer and communication costs, Advisory and Assistance Services contracts, Federally Funded Research and Development Centers and University-Affiliated Research Centers, and Systems Engineering and Integration (SE&I).

Program Manager (PM)—The PAE-designated individual with responsibility for and authority to accomplish program objectives for development, production, and sustainment to meet the user's operational needs for their assigned weapon system. The PM for programs is accountable for credible cost, schedule, performance, and materiel readiness.

Programmed Depot Maintenance—Depot modification and maintenance of all scheduled depot requirements accomplished normally on a calendar time cycle.

Program Office—This office is generally at the program group level and may consist of a PM, item manager, production management specialist, equipment specialist, and financial manager. The single point of contact with industry, government agencies, and other activities participating in the system acquisition process.

Publish Requirements—Requirements are electronically signed by the PSM/PSM designee and published in the approved IT system of record. Each program office will produce a standardized electronic report documenting the validated and prioritized requirements for each program.

Research, Development, Test, and Evaluation—The type of funding, appropriation (3600) intended for Research, Development, Test, and Evaluation efforts. The term "research and development" broadly covers the work performed by a Government agency or the private sector. Research is the systematic study directed toward gaining scientific knowledge or understanding of a subject area. Development is the systematic use of the knowledge and understanding gained from research for the production of useful materials, devices, systems, or methods. Research, Development, Test, and Evaluation includes all supporting test and evaluation activities.

Reliable—Individual tasks developed using a repeatable process that provides a consistent value.

Repair Group Category (RGC)—A single-position, alpha or numeric code that identifies specific commodity or effort groupings of maintenance work requirements.

Requirement—A depot maintenance workload task to assure operational safety, suitability, and effectiveness of a weapon system or commodity, or a validated need satisfied by a buy or repair action required to assure the preservation of baseline characteristics of systems or end items.

Requirement Control Number (RCN)—A six-position numeric code assigned by the IT system of record used to identify individual requirements.

Requirements Validation—PMs, in conjunction with FLDCOM points of contact and the Executive Agent, conduct an annual review of requirements as documented within the approved IT system of record by the applicable PM. These collaborative reviews will ensure requirements are accurate, reliable, timely, properly formatted, documented, and file maintained in the approved IT system of record.

Software Maintenance—Those activities necessary to correct errors in the software, add incremental capability improvements (or delete unnecessary features) through software changes, and adapt software to retain compatibility with hardware or with other systems with which the software interfaces. Software maintenance comprises software maintenance performed on military materiel (e.g., weapon systems and their components, space control systems and their components, automated test equipment and test package sets, and systems integration laboratories).

Source of Repair (SOR)—An industrial complex (organic, commercial contract, or interservice facility) with required technical capabilities to accomplish repair, overhaul, modification, or restoration of specific types of military hardware or software.

Stakeholders—For the purposes of this publication, a stakeholder is an individual or organizational entities (users, developers, acquirers, technologists, testers, budget analysts, sustainers, and industry) that are, or will be, associated with implementing and supporting the associated system, subsystem, or end item capability requirements.

Supportability—The degree to which the planned logistics support allows the system to meet its availability and wartime usage requirements. Planned logistics support includes the following: test, measurement, and diagnostic equipment; spare and repair parts; technical data; support facilities; transportation requirements; training; manpower; and software.

Sustaining Engineering (SE)—Technical tasks to ensure continued operation and maintenance of a system with managed known risk. SE involves the identification, review, assessment, and resolution of deficiencies throughout a system's life cycle. SE both returns a system to its baselined configuration and capability and identifies opportunities for performance and capability enhancement. It includes the measurement, identification, and verification of system technical and supportability deficiencies; associated root cause analyses; evaluation of the potential for deficiency correction; and the development of a range of corrective action options.

Sustainment—The continuing materiel support which consists of the planning, programming, and execution of a logistics support strategy for a system, subsystem, or major end item to maintain operational capabilities from system fielding through disposal.

Technical Data—A general term used when referring to any or all technical publications as a whole or separately, and without reference to any one specific type of publication, such as technical manuals, technical orders, composition, artwork, engineering data, engineering drawings, master layout drawing, un-dimensioned drawings, specifications, parts list, automatic equipment program master tapes or cards, microfilm, printed copies, commercial manuals, film, sound tracks, or any other media used primarily for conveying technical information. The term also applies to the reproducible copy from which copies of technical data are reproduced.

Technical Order (TO)—A publication that gives specific technical directions and information in regard to inspections, storage, operations, modifications, and maintenance of USSF equipment. The various types of technical orders include technical manuals, time compliance technical orders, methods and procedures technical orders, automation type TOs (e.g., tapes and cards that are TO data in digital, magnetic, film, or sound form), index type TOs, and abbreviated TOs.

Then-Year—Refers to obligations (or dollars which will be spent over time).

Timely—Individual tasks identified at the appropriate time to support the requirements development process schedule.

Unfunded Requirement—An identified requirement for which funds are not available to satisfy in the execution year. If funds are not available, the organization must submit an unfunded requirement request for funding consideration.

Variance Narrative—A statement explaining a dollar amount change in a requirement, including what occurred within the program to cause the increase or decrease to the requirement and impacts with reference to the change in quantities, man-hours, or other qualitative details to explain the variance (i.e., historical execution variance, variance from the last year's LRDP requirement position to the current year's LRDP requirement, etc.).


Weapon System—A combination of elements that function together to produce the capabilities required for fulfilling a mission need, including hardware, equipment, software, and all performance-based logistics sustainment elements, but excluding construction or other improvements to real property.

Weapon System Sustainment (WSS)—The continuous support of the weapon system during the Operations and Sustainment phase. There are four business process areas managed as part of WSS: DPEM, CLS, SE, and TOs.

Attachment 2

PROGRAM ENTRY TO WSS DECISION TREE

Figure A2.1. Program Entry to WSS Decision Tree.

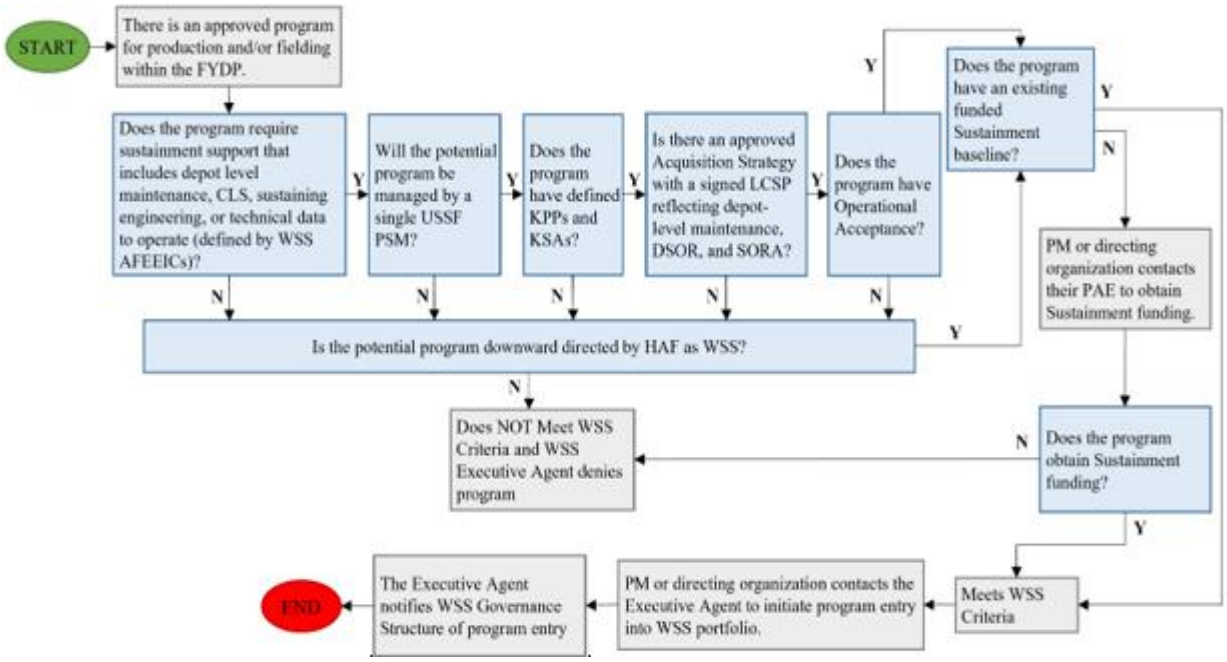

A2.1. Decision Tree Terms and Criteria Descriptions.

A2.1.1. Weapon System Sustainment. WSS is a subset of readiness funding, which includes four business process areas: CLS, DPEM, SE, and TOs. The type of sustainment support is documented through an approved Product Support Strategy.

A2.1.2. Single USSF PSM. On behalf of PAEs, WSS PSMs are responsible for all assigned programs or weapon systems in sustainment.

A2.1.3. Key Performance Parameters (KPPs) and Key System Attributes (KSAs). KPPs and KSAs must be pre-determined for a program prior to entering the WSS portfolio. KPPs are critical system capabilities a weapon system must meet to achieve operational goals and are considered vital to the system's performance, function, design, and operations. KSAs are vital, but not critical, system capabilities a weapon system must possess in support of meeting its KPPs.

A2.1.4. Life Cycle Sustainment Plan (LCSP). The LCSP is an official document that describes overall acquisition and program management strategies, as well as the life cycle sustainment support strategy.

A2.1.5. Depot Source of Repair (DSOR) and Source of Repair Assignment (SORA). DSOR is the method by which the Department of Defense postures its depot-level maintenance workloads – organic, contract, or a combination of both. The PM collaborates with the Executive Agent to determine the core depot-level maintenance and repair requirements. Additional information on DSOR and SORA is referenced in DAFMAN 63-122, *Depot Source of Repair Planning and Activation*.

A2.1.6. Operational Acceptance (OA). Programs who gain OA are considered to have met operational requirements and have the necessary elements required to support mission execution. Additional information on the OA process is referenced in Space Force Instruction 13-604, *System Acceptance*.

A2.1.7. Downward Direction by HQ DAF. If a potential program is considered for downward direction by HQ DAF, the program's sustainment requirements, anticipated risk, and identified sustainment funding are required to be presented to the corporate structure for senior leaders to make the decision.

A2.1.8. Funded Sustainment Baseline. A capability or program requiring sustainment support, regardless of acquisition method, must have a fully funded sustainment baseline prior to entry into the WSS portfolio. A fully funded baseline ensures sustainment needs are adequately considered prior to fielding. For example, initial O&M WSS funding is documented in the Program and Budget Enterprise Service budget line with Program Element Code details.

A2.2. AFEEICs. The AFEEICs for consideration into the WSS portfolio are 540XX, 544XX, 560XX, 578XX, 583XX, and 594XX.

Attachment 3

RISK CATEGORY DESCRIPTIONS

A3.1. Explanation of Risk Categories.

A3.1.1. CLS Spares.

A3.1.1.1. Category Description.

A3.1.1.1.1. This category includes cost of replenishing or repairing initial spares stock.

A3.1.1.1.2. Repairments may include the following: reparable individual parts, assemblies or subassemblies that are required on a recurring basis for the repair of major end items of equipment; consumable repair parts, assemblies, subassemblies, and material consumed in the field maintenance; or the repair of a major system, associated support equipment, and unit-level training devices.

A3.1.1.1.3. This also includes the costs incurred to replace equipment that is needed to operate or support Space weapon systems and other associated support equipment.

A3.1.1.1.4. WSS does not fund initial spares procurement.

A3.1.1.2. File Maintenance Requirements.

A3.1.1.2.1. Ensure the appropriate SAF/FM AFEEIC 578 shred is used for each task and sub-task in order to capture the predominate type of CLS activity being accomplished and the predominate method of accomplishment per the AFEEIC definitions.

A3.1.1.2.2. Costs must be allocated among respective systems if the support equipment being replaced (e.g., tools, test sets, etc.) is common to multiple systems.

A3.1.1.2.3. CLS spares requirements are file maintained in dollars.

A3.1.2. On-Orbit Support.

A3.1.2.1. Category Description. This category is defined as CLS-funded contractors directly supporting the operation of Space weapon systems, including on-console operators, contracted operations floor technical advisors, and contractors specifically dedicated to anomaly resolution of On-Orbit assets in a factory reach-back capability.

A3.1.2.2. File Maintenance Requirements.

A3.1.2.2.1. Any sustaining engineering efforts not directly related to On-Orbit Support will be captured in AFEEICs 57834 or 58300 as applicable.

A3.1.2.2.2. On-Orbit Support requirements are file maintained in dollars.

A3.1.3. Other Major End Items (OMEI).

A3.1.3.1. Category Description. OMEI requirements are defined as depot-level hardware maintenance, to include repair work, which utilize Repair Group Category (RGC) G for programmed workload or RGC H for unprogrammed workload (i.e., hardware repaired on an as needed basis). This applies to all work performed using military personnel, Government civilian personnel, interservice agreement, or CLS contractor personnel. Requirements in this category include programmed depot maintenance, urgent depot-level maintenance/emergency depot-level maintenance, depot field teams, and contract field teams. Communication-Electronic OMEI requirements follow the Communication-Electronic schedule review process contained in TO 00-25-108, *Communications-Electronics (C-E) Depot Support*.

A3.1.3.2. File Maintenance Requirements. AFEEIC 54401 scheduled requirements (RGC G) are file maintained in hours. Other AFEEICs and unscheduled requirements are documented in dollars.

A3.1.4. Software.

A3.1.4.1. Category Description.

A3.1.4.1.1. Software maintenance requirements include organic and contracted software embedded in space weapon systems, including RGC S for organic depot software maintenance. Software maintenance requirements are changes designed to correct errors or deficiencies, improve performance within existing specifications, or adapt to a changing environment.

A3.1.4.1.2. The USSF utilizes organic software engineers, contractors, interservice, or a combination, depending on the DSOR, to determine the best solution for software maintenance performance.

A3.1.4.2. File Maintenance Requirements.

A3.1.4.2.1. Document software project or block cycle schedules to include as much detail and definition of the project as possible. All known elements such as urgent or emergency software updates, lab sustainment, initial deficiency investigations, and customer support (i.e., computability investigations, documentation reviews, phone, email support, or site visits – not necessarily related to currently fielded software) of each software project or block cycle should be documented within the requirement.

A3.1.4.2.2. If the software project or block cycle work is accomplished using both organic and contract, there should be one requirement for each SOR, and both requirements should reference each other.

A3.1.4.2.3. Organic software requirements are file maintained in man-hours.

A3.1.4.2.4. Contract software requirements are file maintained in dollars.

A3.1.5. Sustaining Engineering (SE).

A3.1.5.1. Category Description.

A3.1.5.1.1. WSS funded SE requirements are those engineering efforts required to review, assess, define, and resolve technical or supportability deficiencies revealed in fielded systems, products, and material. The objective of SE is to assess and determine sustainment solutions for the fielded system, product, or material to the approved specification capability. WSS SE efforts may lead to development or production engineering efforts, which would not be considered WSS.

A3.1.5.1.2. Examples of WSS funded SE activities include, but are not limited to: analysis of system or materiel deficiencies; diminishing manufacturing sources and material shortages; aging and surveillance testing; environmental protection directives (i.e., Environment, Safety, and Occupational Health; and Programmatic Environmental Safety and Occupational Evaluation) hazard identification, risk assessment, and mitigation measures; failure analysis; mishap and safety investigations; reverse engineering; engineering studies to identify the depth of, and replacement solutions for, unsupportable sub-systems or components; engineering analysis to support Federal Aviation Administration requirements; regression analysis of prototypes and test articles; cyber Risk Management Framework accreditation; supply chain risk management; and computer modeling for the purpose of validating solutions.

A3.1.5.2. File Maintenance Requirements.

A3.1.5.2.1. The requirement should explain the deficiency in terms of impact, solution, or deliverables as well as the work to fix it to include start and stop dates for the tasks when possible. Requirements should be consistent with start and stop dates.

A3.1.5.2.2. Organic AFEEIC 583OR SE task requirements are documented in hours, as well as dollars. When using this AFEEIC, the reference RCN and SOR must be identified in the requirement attributes section.

A3.1.5.2.3. SE requirements are file maintained in dollars.

A3.1.6. Technical Orders (TOs).

A3.1.6.1. Category Description.

A3.1.6.1.1. TO requirements are categorized as labor, distribution, or improvements. Policy direction for TOs is provided in DAFI 63-101/20-101; TO 00-05-01, *Air Force Technical Order System*; TO 00-05-03, *Air Force Technical Order Life Cycle Management*; and TO 00-05-15, *Air Force Time Compliance Technical Order Process*. Official guidance on funding technical data requirements is found in DAFMAN 65-605, *Vol 1, Budget Guidance and Technical Procedures*.

A3.1.6.1.2. WSS funds are used to ensure currency of TOs for fielded USSF systems and equipment, including activities such as converting source data to standard USSF formats (e.g., S1000D), preparing changes, completing revisions, shipping of compact discs or digital versatile discs and printing TOs on traditional paper. Program offices should refer questions on funds usage to the local FM organization.

A3.1.6.2. File Maintenance Requirements.

A3.1.6.2.1. Conversion requirements should be identified as a separate requirement.

A3.1.6.2.2. If a TO information sheet is the basis of estimate, a Microsoft Excel file must be attached to show the basis of the estimate or provide a Comprehensive Air Force TO Plan to the respective WSS analyst.

A3.1.6.2.3. O&M Element of Expense Investment Code 594 requirements for a specific TO use only one Program Element Code.

A3.1.7. Training.

A3.1.7.1. Category Description.

A3.1.7.1.1. WSS funded training requirements include costs to provide USSF weapon system training, including costs of instructors, training support personnel, training devices, course support costs, and course materials.

A3.1.7.1.2. This category also includes costs to provide, operate, and maintain onsite or centralized USSF weapon system simulator training devices, including labor, materials, and overhead costs of simulator operations by military and/or Government civilian personnel where paid or reimbursed through a CLS contract.

A3.1.7.1.3. Personnel travel for training and associated temporary additional duty or temporary duty costs are not included in this risk category.

A3.1.7.2. File Maintenance Requirements. Training requirements are file maintained in dollars.

A3.1.8. CLS Management.

A3.1.8.1. Category Description. CLS Management is a method of contracting WSS support for a program, system, subsystem, training system, equipment, or item used to provide all or part of the product support elements in direct support of the approved sustainment strategy. Therefore, this risk category captures all WSS requirements not included in the above commodity-based categories.

A3.1.8.2. File Maintenance Requirements. Ensure the appropriate SAF/FM AFEEIC 578 shred is used for each task and sub-task in order to capture the predominate type of CLS activity being accomplished and the predominate method of accomplishment per the AFEEIC definitions.

A3.2. AFEEICs. The official definitions of AFEEIC attributes are located within the Financial Management Data Quality Service at **https://fmdqs.cce.af.mil/saml/home.htm**.

Attachment 4

PROGRAMMATIC FAILURE POINT DEFINITIONS

Table A4.1. Programmatic Failure Point Definitions by Risk Category.

Risk Category	Failure Definition
CLS Management	Does not meet contractually defined programmed and/or scheduled hours, performance objectives, or required minimal level of effort; less than defined contractual programmed and/or operational requirements.
CLS Spares	Does not meet contractually defined programmed and/or scheduled hours, performance objectives, or required minimal level of effort; less than defined contractual programmed and/or operational requirements.
On-Orbit Support	Does not meet contractually defined programmed and/or scheduled hours, performance objectives, or required minimal level of effort; less than defined contractual programmed and/or operational requirements.
OMEI	Occurs when OMEI repair(s) falls below program or system minimal operational availability standard and/or falls below operational requirement to meet mission needs.
Software	Inability to maintain core capability sufficient to correct urgent and emergency software updates which may, include but not limited to, specialized skills and expertise, data, infrastructure (e.g., software lab), information assurance (e.g., authority to operate), the inability to fix CAT I deficiencies; includes safety, mandates (e.g., cyber security), and mission critical.
SE	The inability to support engineering efforts required to meet defined minimal performance objectives and to ensure the mandatory requirements of Operational, Safety, Suitability, & Effectiveness measures.
TOs	Cannot produce and distribute emergency or urgent TO change requests.
Training	The point where the program is unable to meet minimum requirements (e.g., readiness, relevance, realism, etc.), which will result in failure to meet minimum availability and minimum student production.

Attachment 5

REQUIREMENT CHANGE THRESHOLD AND APPROVAL CRITERIA

Table A5.1. Requirement Change Threshold and Approval Criteria.

Requirement Change Type	Role Threshold	Requirement Change Criteria	
		% and $K	or $K
Buy Down	Program Approval	No threshold (100% review)	
	Executive Agent Analyst		
	Executive Agent Chief		
Contract Price Change	Program Approval	15% and $200 (min)	$500
	Executive Agent Analyst	15% and $200 (min)	$500
	Executive Agent Chief	15% and $200 (min)	$500
Deferral	Program Approval	No threshold (100% review)	
	Executive Agent Analyst		
	Executive Agent Chief		
Scope Change	Program Approval	15% and $200 (min)	$500
	Executive Agent Analyst	15% and $200 (min)	$500
	Executive Agent Chief	15% and $200 (min)	$500
Unexecutable	Program Approval	15% and $200 (min)	$500
	Executive Agent Analyst	15% and $200 (min)	$500
	Executive Agent Chief	15% and $200 (min)	$500
Unpublished	Program Approval	No threshold (100% review)	
	Executive Agent Analyst		
	Executive Agent Chief		
Previous Buy Down	Program Approval	No threshold (100% review)	
	Executive Agent Analyst		
	Executive Agent Chief		
Previous Deferral	Program Approval	No threshold (100% review)	
	Executive Agent Analyst		
	Executive Agent Chief		

Attachment 6

EMERGING SPACE REQUIREMENTS

A6.1. Emerging Space Overview.

A6.1.1. The purpose of the Emerging Space initiative is to capture future WSS requirements for space programs and systems fielding within the FYDP, regardless of acquisition method, allowing USSF to plan and program resources for fully burdened requirements.

A6.1.2. To support the Emerging Space initiative, WSS uses the ESR program group to show full requirement values in a manner that does not conflict with the sustainment of legacy weapon systems.

A6.1.2.1. The ESR program group informs the sustainment community of the scope and size of new program or system requirements and allows USSF to advocate for sufficient FYDP funding.

A6.1.2.2. The requirements captured in the ESR program group remain unfunded in WSS until the program or system is onboarded into the portfolio. At the time of onboarding, the program or system is transferred into its own WSS program group.

A6.1.2.3. The ESR program group is excluded from WSS portfolio-level risk assessments.

A6.1.3. The Emerging Space initiative requires active involvement by, and coordination between, both the "losing organization" and "gaining organization" of an emerging program or system. For the purpose of the WSS Emerging Space initiative:

A6.1.3.1. A program or system in Emerging Space is defined to include systems, subsystems, systems of systems, end items, services, or activities that provide an increased operational capability and require sustainment funding upon fielding.

A6.1.3.2. Fielding, during this process, is the key transition point when a program or system achieves OA. This may happen as full OA, or it may happen incrementally with an initial operational capability decision and multiple follow-on designated operational capability deliveries.

A6.1.3.3. The losing organization is defined as the entity that acquires new programs or systems to be transferred into the WSS portfolio. The losing organization will plan, program, and budget for the support requirements through the FYDP, providing a fully burdened sustainment baseline that will transition upon fielding. **(T-1)**

A6.1.3.4. The gaining organization is defined as the entity supporting fielded, legacy programs or systems and responsible for planning, programming, budgeting, and executing support requirements beyond the fielding date. The gaining organization must utilize the ESR program group to capture future WSS requirements. **(T-1)**

A6.2. Requirements Rule Set.

A6.2.1. All requirements must meet the entrance criteria for WSS as defined in **Attachment 2**, Program Entry to WSS Decision Tree, regardless of acquisition method.

A6.2.1.1. Requirement acquisition methods include traditional Joint Requirements Oversight Council acquisition, rapid prototype and fielding process (National Defense Authorization Act Sec 804) acquisition, and other transaction authority funds-acquired programs or systems (see DAFI 63-101/20-101 for more information).

A6.2.1.2. Requirements also include service transfers of fielded weapon systems, as well as operationalized prototypes or directed initiatives that provide additional capability to a fielded weapon system.

A6.2.2. The Executive Agent acts as the overall process owner of the ESR program group and will assign program office personnel to identify and maintain their own emerging requirements.

A6.2.3. Program offices are responsible for building their Emerging Space requirements in this group using full requirement values to ensure FYDP concerns are collaborated on by all parties involved and sustainment needs are adequately considered during the acquisition phase.

A6.3. Requirements Process. The ESR process, as depicted in **Figure A6.1**, outlines the communication, coordination, and funds transfer actions required between the losing organization and gaining organization for an emerging program or system.

Figure A6.1. Emerging Space Requirements Process.



A6.3.1. POM Year +2 (at minimum).

A6.3.1.1. Losing Organization. In relation to DAFI 63-101/20-101 guidance on lifecycle management, the losing organization is responsible for identifying the sustainment needs of the emerging program or system to transition into WSS. The organization must plan and program for full and complete sustainment funding in accordance with the most credible, approved cost estimate (i.e., single best estimate, non-advocate cost assessment, service cost position, etc.) as soon as possible, but no later than POM Year +2. **(T-1)** The POM submission incorporates an entire sustainment baseline through the FYDP.

A6.3.1.1.1. The losing organization coordinates with the gaining organization to ensure agreement on estimated sustainment costs for the program or system, to include potential offset values.

A6.3.1.1.2. The losing organization must submit an initiative in their POM to capture the initial sustainment baseline to align with the approved cost estimate values using appropriation 3410, cost category 554WT, and a sustainment Program Element Code. **(T-1)**

A6.3.1.2. Gaining Organization. The gaining organization is responsible for supporting the losing organization in their POM submission to ensure fully burdened Sustainment needs are captured.

A6.3.1.2.1. The gaining organization identifies and coordinates potential offset values for legacy programs or systems being replaced.

A6.3.1.2.2. The gaining organization creates new RCNs in the ESR program group with full requirement values to align with the approved cost estimate. In the absence of an approved cost estimate, the gaining organization must submit a placeholder requirement to capture the emerging program or system. **(T-1)**

A6.3.2. POM Year +1.

A6.3.2.1. Losing Organization.

A6.3.2.1.1. The losing organization must submit a disconnect in their POM to capture the difference between the established sustainment baseline and the refined approved cost estimate. **(T-1)**

A6.3.2.1.2. The losing organization obtains the offset values for the fielded program or system being replaced from the gaining organization to incorporate into their POM disconnect submission.

A6.3.2.2. Gaining Organization.

A6.3.2.2.1. The gaining organization coordinates established offset values with the losing organization.

A6.3.2.2.2. The gaining organization consolidates all offset requirement values into one sustainment requirement in the legacy program group.

A6.3.2.2.3. The gaining organization must adjust the requirements to the full value of the program or system in the ESR program group to align with the refined approved cost estimate. **(T-1)**

A6.3.3. POM Year.

A6.3.3.1. Losing Organization.

A6.3.3.1.1. The losing organization must submit a disconnect in their POM to capture the difference between the established sustainment baseline and the approved cost estimate. **(T-1)**

A6.3.3.1.2. The losing organization must submit a zero-based transfer (ZBT) for approval from SFCS to reprogram funds from their designated OAC and cost category 554WT into OAC S7. **(T-1) The** losing organization coordinates with the gaining organization for accounting elements to align ZBT funds with established requirements.

A6.3.3.2. Gaining Organization.

A6.3.3.2.1. The gaining organization must refine the requirements to the full value of the program or system in the ESR program group to align with the approved cost estimate. **(T-1)**

A6.3.3.2.2. The gaining organization coordinates with the losing organization for accounting elements to align ZBT funds with established requirements.

A6.3.3.2.3. The gaining organization must communicate the emerging program or system through their programmatic review briefing to validate sustainment funds are sufficient and support the losing organization's ZBT. **(T-1)**

A6.3.4. Upon OAC ZBT Approval.

A6.3.4.1. Gaining Organization.

A6.3.4.1.1. During LRDP, the gaining organization must request a standalone WSS program group to align the new program or system. **(T-1)**

A6.3.4.1.2. Once the new WSS program group is created, the gaining organization will transfer requirements from the ESR program group and zero out the offset requirement in the legacy program group. **(T-1)**

A6.3.4.2. Executive Agent. During LRDP, the Executive Agent approves and establishes the new WSS program group to align the new program or system.

A6.3.5. Budget Year.

A6.3.5.1. Losing Organization. The losing organization is responsible for funding interim contractor support for OA liens (e.g., issues found in final testing, resolution for obsolescence and diminishing manufacturing sources and material shortages, etc.).

A6.3.5.2. Executive Agent. The Executive Agent conducts the initial funds spread, applying the ZBT and offset funds to the new WSS program group, and verifies the gaining organization's realignment of funds maintains the baseline.

A6.3.5.3. Gaining Organization. The gaining organization must realign the initial funds spread, ensuring the transferred baseline funding level is maintained. **(T-1)**
